


Activity Description	Orig Dur	%	Early Start	Early Finish	2007 2008 2009 2010 2011																			
					2007				2008				2009				2010				2011			
					Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
<b>EL CAJON VALLEY HS</b>																								
<b>2B - Modernization</b>																								
<b>Construction Phase</b>																								
Start Construction Phase	0	100	03JUL07A																					
Construction Phase Bldg. 500	193	100	03JUL07A	07JAN08A																				
Construction Phase Bldg. 100	115	50	08JAN08A	26APR08																				
Construction Phase Bldg. 200	95	0	27APR08	31JUL08																				
Substantial Completion Milestone	0	0		01JUL08																				
<b>Close-Out Phase</b>																								
Start Close Out Phase	0	0	01AUG08																					
Punch List Items	30	0	01AUG08	11SEP08																				
File NOC w/ County / DSA 90 Day Letter	30	0	01AUG08	11SEP08																				
Final Walk Through	5	0	12SEP08	18SEP08																				
DSA Final Close Out	0	0		18SEP08																				



GROSSMONT UNION HIGH SCHOOL DISTRICT  
 PROPOSITION H BOND PROGRAM  
 El Cajon Valley High Layout

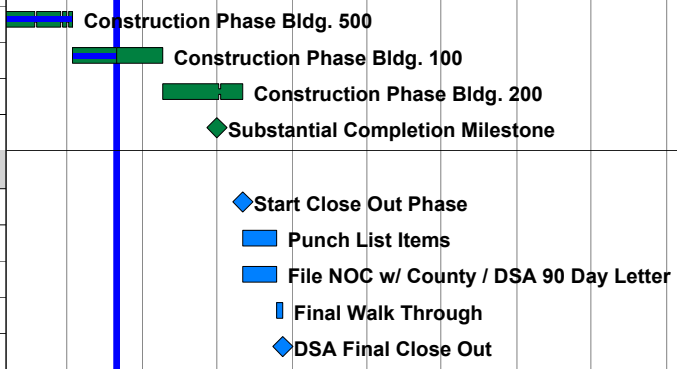
