


Activity Description	Orig Dur	%	Early Start	Early Finish	2007	2008				2009				2010				2011				2012
					Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1

# HELIX HS

## 3A - New Construction

Pre-Design / Programming Phase				
Pre-Design Phase	1	100	28JAN08A	08FEB08A
Design Phase				
Schematic Design Phase	20	70	11FEB08A	07MAR08
Start Design Phase	0	100	11FEB08A	
Design Development Phase	20	0	10MAR08	04APR08
Construction Document Phase	30	0	07APR08	16MAY08
Design Ready for DSA Submission	0	0		16MAY08
DSA Phase				
Start DSA Phase	0	0	16JUN08*	
DSA Submittal / Review Phase	35	0	16JUN08	01AUG08
Constructability Review	30	0	04AUG08	12SEP08
DSA Back Check / Approval	30	0	04AUG08	12SEP08
DSA Review Complete	0	0		12SEP08
Bid / Award Phase				
Start Bid / Award Phase	0	0	22SEP08	
Prepare Bid Package	10	0	22SEP08	03OCT08
1st Advertisement	5	0	06OCT08	10OCT08
Job Walk	1	0	13OCT08	13OCT08
2nd Advertisement	5	0	14OCT08	20OCT08
Job Walk	1	0	23OCT08	23OCT08
Bid Opening	0	0		23OCT08
Protest Period / NOI Letter	5	0	24OCT08	30OCT08
Award Contract	10	0	03NOV08	14NOV08
Bid Phase Complete	0	0		24NOV08
Construction Phase				
Start Construction Phase	0	0	08DEC08	
Construction Phase	455	0	08DEC08	08MAR10
Substantial Completion Milestone	0	0		08FEB10
Close-Out Phase				
Start Close Out Phase	0	0	09MAR10	
Punch List Items	30	0	09MAR10	19APR10
File NOC w/ County / DSA 90 Day	30	0	09MAR10	19APR10
Final Walk Through	5	0	20APR10	26APR10

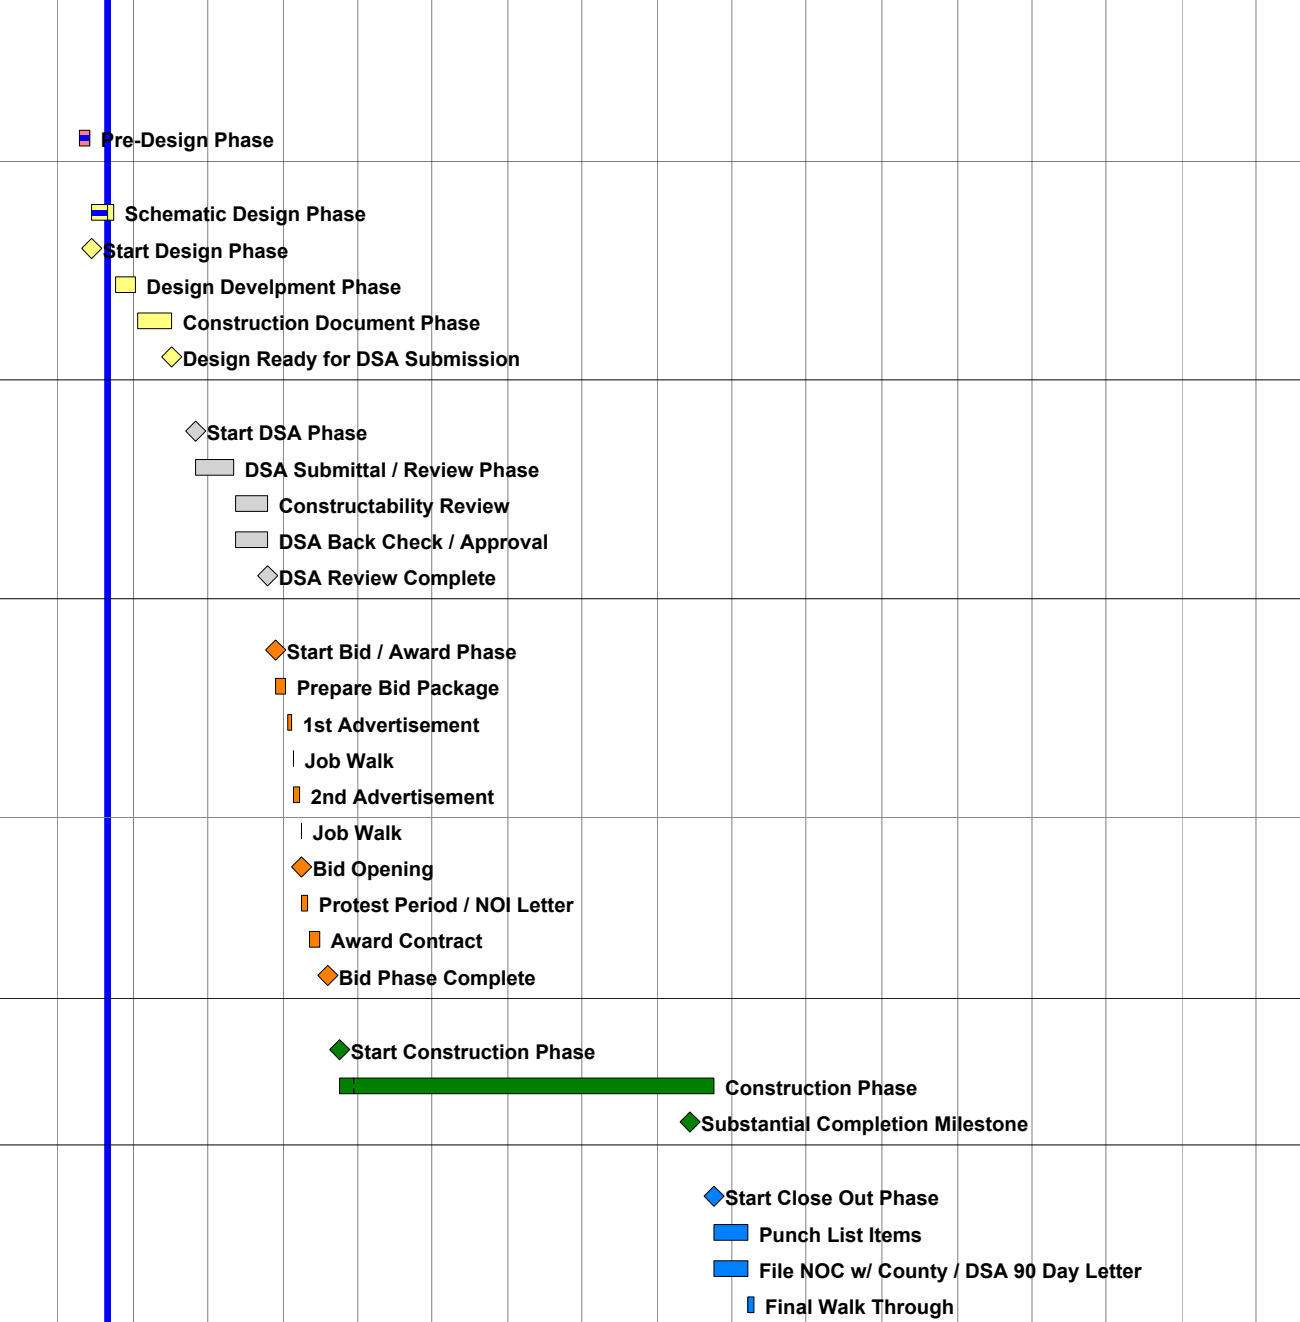

GROSSMONT UNION HIGH SCHOOL DISTRICT  
 PROPOSITION H BOND PROGRAM  
 Helix Charter High Layout

Project Phase	
<span style="color: pink;">■</span>	Pre-Design / Programming Phase
<span style="color: yellow;">■</span>	Design Phase
<span style="color: grey;">■</span>	DSA Phase
<span style="color: orange;">■</span>	Bid / Award Phase
<span style="color: green;">■</span>	Construction Phase
<span style="color: blue;">■</span>	Close-Out Phase

