

Activity Description	Orig Dur	%	Early Start	Early Finish	2007 2008 2009 2010 2011																			
					2007				2008				2009				2010				2011			
					Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3

MOUNT MIGUEL HS

2A - Infrastructure

Pre-Design / Programming Phase

Pre-Design / Programming	30	100	21MAY07A	14JUN07A
--------------------------	----	-----	----------	----------

Design Phase

Start Design Phase	0	100	13AUG07A	
Schematic Design Phase	20	100	13AUG07A	09OCT07A
Design Development Phase	25	100	10OCT07A	04DEC07A
Construction Document Phase	25	100	05DEC07A	30JAN08A
Design Ready for DSA Submission	0	100		30JAN08A

DSA Phase

DSA Submittal / Review Phase	30	75	04FEB08A	11MAR08
Start DSA Phase	0	100	04FEB08A	
Constructability Review	10	0	12MAR08	25MAR08
DSA Back Check / Approval	20	0	12MAR08	08APR08
DSA Review Complete	0	0		08APR08

Bid / Award Phase


Start Bid / Award Phase	0	0	09APR08	
Prepare Bid Package	1	0	09APR08	09APR08
1st Advertisement	5	0	14APR08	18APR08
Job Walk	1	0	23APR08	23APR08
2nd Advertisement	5	0	24APR08	30APR08
Job Walk	1	0	05MAY08	05MAY08
Bid Opening	0	0		05MAY08
Protest Period / NOI Letter	5	0	06MAY08	12MAY08
Award Contract	10	0	13MAY08	26MAY08
Bid Phase Complete	0	0		26MAY08

Construction Phase

Start Construction Phase	0	0	27MAY08	
Construction Phase	100	0	27MAY08	13OCT08
Substantial Completion Milestone	0	0		15SEP08

Close-Out Phase

Start Close Out Phase	0	0	14OCT08	
Punch List Items	30	0	14OCT08	24NOV08
File NOC w/ County / DSA 90 Day Letter	10	0	28OCT08	10NOV08
Final Walk Through	2	0	11NOV08	12NOV08
DSA Final Close Out	0	0		12NOV08

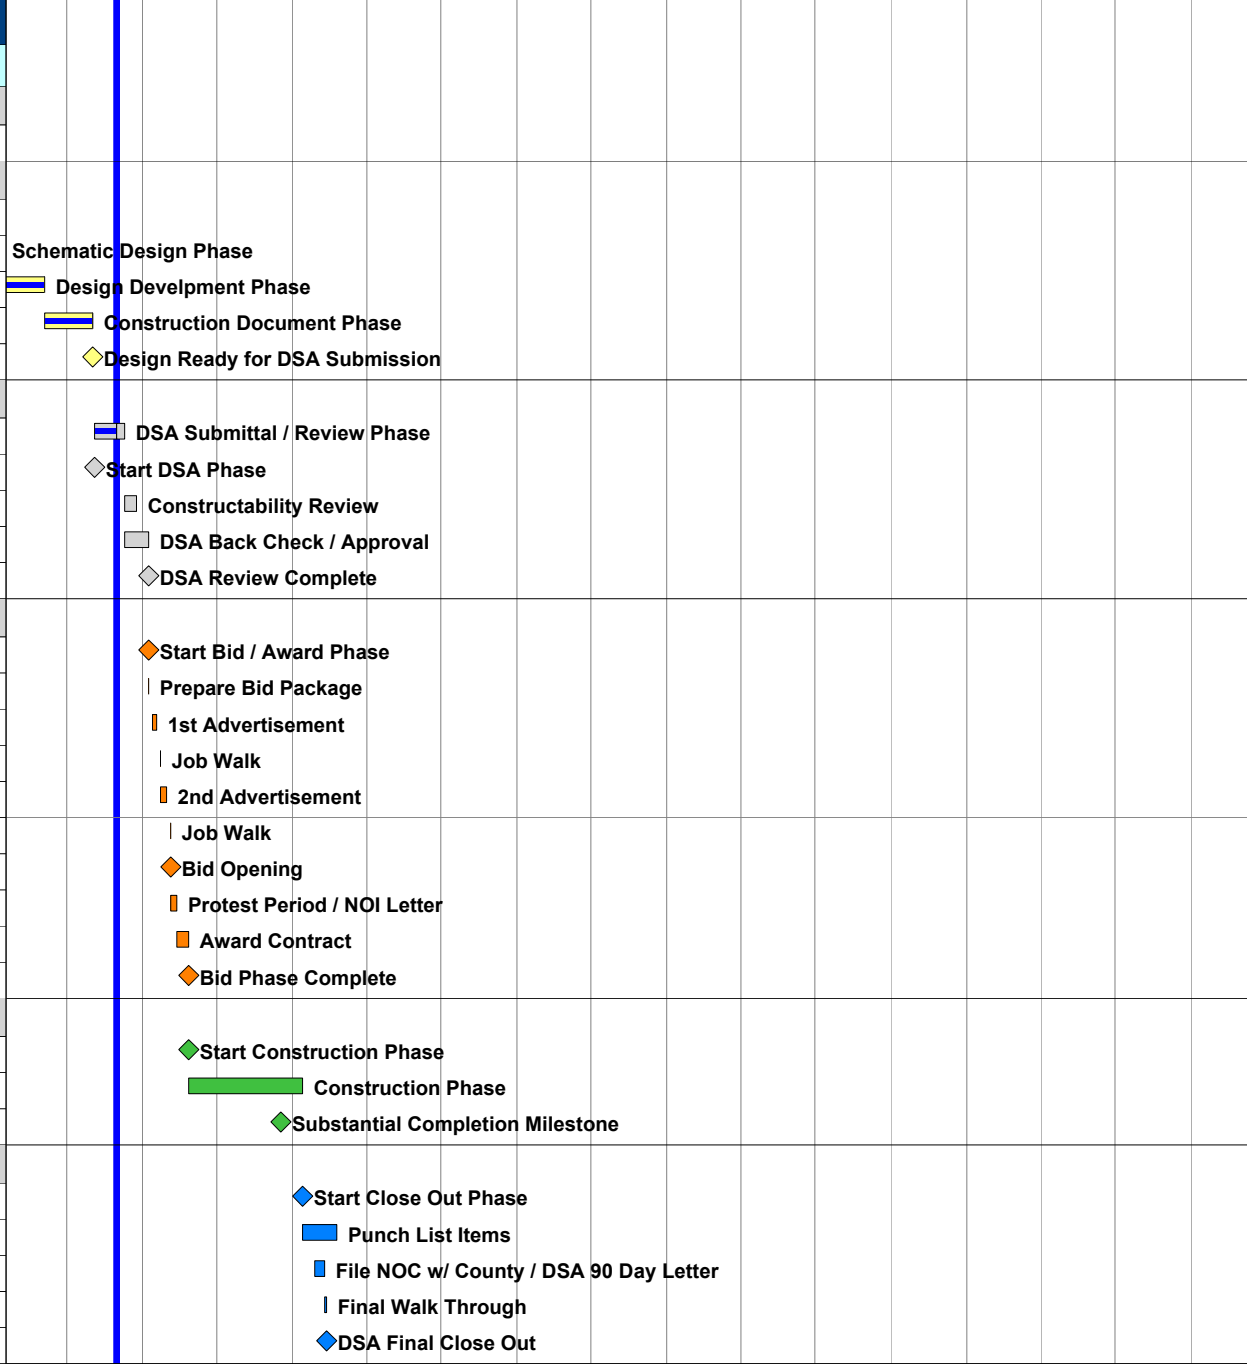

GROSSMONT UNION HIGH SCHOOL DISTRICT
 PROPOSITION H BOND PROGRAM
 Mount Miguel High Layout

Project Phase	
	Pre-Design / Programming Phase
	Design Phase
	DSA Phase
	Bid / Award Phase
	Construction Phase
	Close-Out Phase
