



GROSSMONT UNION HIGH SCHOOL DISTRICT Proposition H Bond Program October 2007 Progress Report



Grossmont HS – Bldg. 800



El Cajon Valley HS – Bldg. 500

Prepared on behalf of:

R. F. Kiesling
Executive Director
Facilities Management

Governing Board Members:

Richard Hoy
Jim Kelly
Priscilla Schreiber
Robert Shield
Larry Urdahl

Superintendent:

Robert J. Collins

Deputy Superintendent,

Business Services:

Scott Patterson

PERIOD COVERED:

October 1 thru 31, 2007

FISCAL YEAR

FY0708

PROGRESS REPORT NO.

PR-001-07/08-01





TABLE OF CONTENTS

- 1.0 Executive Summary**
 - 1.1 Program Summary
 - 1.2 Program Highlights/Key Milestones
 - 1.3 Look Ahead (next 90 days)
 - 1.4 Key Issues

- 2.0 Project Status Report – “Active” Projects**
 - 2.1 Budget; Funding; Scope; Issues; % Complete by Phase; Photos

- 3.0 Master Program Schedule**
 - 3.1 Master Summary Schedule By School
 - 3.2 Master Project Detail Schedule By School

- 4.0 Financial (*future*)**
 - 4.1 Budget vs. Funding (Project I.D. Specific; District/Program Summary)
 - 4.2 Budgets vs. Actual (Project I.D. Specific; District/Program Summary)
 - 4.3 Project Budget Detail Worksheet – Budget Changes (Proposed/Approved)
 - 4.4 Budget vs. Actual (Forecast Cost at Complete)

- 5.0 Statistical Data**
 - 5.1 Charts; Graphs

- A. Appendices**
 - Proposition H – School Weekly Activity Report (SAMPLE REPORT)



1.0 Executive Summary



1.0 EXECUTIVE SUMMARY

1.1 Program Summary

- The Proposition H Program is currently poised and on the verge of going “full throttle” with classroom modernization construction across seven (7) school sites simultaneously. With Phase 2 B construction already underway at Grossmont HS and El Cajon Valley HS (since July 2007) and Phase 2B construction imminently pending at Granite Hill HS, Helix HS, El Capitan HS, Monte Vista HS, and Santana HS, we are literally moving into a “classroom modernization phase” (190 classrooms) unprecedented in the history of the District.
- Santana HS (Phase 2B) bid opening has been delayed as a result of the fires, but, we are expecting a recommendation to award contracts to go before the Board in December 2007, with construction to commence by year end on 24 classrooms.
- In total, Phase 2B will modernize 293 classrooms, with the balance of classrooms to be modernized at Mount Miguel HS (46 classrooms), and Valhalla HS (33 classrooms). Those projects have recently commenced with the “Design Phase”, and will move into construction during 2008.
- With the arrival of the program manager, we have been in a position to make significant headway on several fronts; first, in terms of a realignment of roles & responsibilities, and second, our architectural and construction management contract agreements have undergone complete overhauls, with more definite scopes of services, target construction budgets, task order budgets, deliverables schedules, and monthly progress reports. We have also benefited by the successful negotiation of fee discounts for architectural services on the Science Building (Phase 3A) projects.
- With Phase 2B significantly into the “construction phase”, and Phase 3A into the “design phase”, and Phase 3BR into the “planning, predesign phase”, we have established a “new momentum” and thus, created a renewed sense of urgency for the program.
- Regarding the ultimate decision of how best to commit and expend the \$65M of New School (NS)/Phase 3C funding, we are gathering the data necessary to formulate a recommendation as to how best to proceed to ultimately meet the objectives of fulfilling the “facilities needs” of the District.
- In October, we launched the Proposition H – School Weekly Activity Report (SWAR) which is intended to serve as an effective “snapshot” communication tool at each school site. See example in Appendix section.
- We look forward to providing this monthly progress report as a means of keeping project participants, the District’s Governing Board, the Citizen’s Bond Oversight Committee, and community members informed of progress on the implementation of the Proposition H bond program.



1.2 Program Highlights/Key Milestones

- It is the intent of this section of the progress report that you will find program highlights and key milestones relative to each “active” project.

Close-out/Commissioning Phase

- No activity on major Proposition H phase projects.
- All Phase 1/2A projects were previously closed out with the exception of Mount Miguel which is in the design phase.

Construction Phase

- Grossmont HS (Phase 2B)** – The 800 Building is scheduled for completion and turnover on November 15, 2007, however, due to the fires, this phase will likely be impacted by 7 days.
- El Cajon Valley HS (Phase 2B)** – The 500 Building is scheduled for completion and turnover on November 15, 2007, however, due to the fires, this phase will likely be impacted by 7 days.
- Granite Hills HS (Phase 2B)** – Notices to proceed have been issued and the trade contractors are mobilizing.
- Helix HS (Phase 2B)** – The preconstruction meetings were delayed due to the fires, but, notices to proceed have been issued and the trade contractors are mobilizing.

Bid/Award Phase

- El Capitan HS (Phase 2B)** – The bid opening was October 16, 2007; anticipate award date of November 8th.
- Monte Vista High School (Phase 2B)** – The bid opening was held on October 30, 2007, delayed 1 week as a result of the fires. Anticipate award date of November 8th.
- Santana High School (Phase 2B)** – The bid opening is scheduled for November 8th, having been delayed as a result of the fires. Anticipate award date of December 13th.

Design Phase

- Grossmont High School (Phase 3A) – New Science Buildings** – Schematic Design commenced in October 2007. Harley Ellis Devereaux is the Architect of Record.
- Helix High School (Phase 3A) – New Science Building** – Schematic Design commenced in October 2007. Harley Ellis Devereaux is the Architect of Record.
- El Cajon High School (Phase 3A) – New Science Building** – Schematic Design commenced in October 2007. HMC Architects is the Architect of Record.
- Mount Miguel High School (Phases 1A) – Underground Utility Infrastructure; (Phase 2B)** – Schematic Design commenced simultaneously in October 2007. Mele Amantea Architects is the Architect of Record.
- El Capitan High School (Phase 3A) – New Science Building** – Schematic Design commenced in October 2007. Harley Ellis Devereaux is the Architect of Record.
- Granite Hills High School (Phase 3A) – New Science Building** – Schematic Design commenced in October 2007. HMC Architects is the Architect of Record.



- **Monte Vista High School (Phase 3A) – New Science Building** - Schematic Design commenced in October 2007. Harley Ellis Devereaux is the Architect of Record.
- **Valhalla High School (Phase 2B, 3A, 3BR)** - Schematic Design commenced in October 2007. Platt-Whitelaw Architects is the Architect of Record.
- **West Hills High School (Phase 2B)** - Schematic Design commenced in October 2007. Harley Ellis Devereaux is the Architect of Record.

Planning/Pre- Design Phase

- **Phase 3BR** - This follow on phase of classroom building modernizations is currently in the final prioritization, scoping phase to determine how best to commit the representative funds at each school site.
- **Chaparral High School (Phase 2B)** – The final scoping is currently being finalized and this project is expected will move into design next month.
- **Viking Center** – Modernization vs. Demolition/Replacement discussions are continuing to be analyzed with several scenarios being considered.

1.3 Look Ahead (next 90 days)

- The significant events that are scheduled or are targeted to occur in the next 90 days are as follows:

Management Recommendations Tracking Tool – We will continue our diligent efforts to manage all recommendations (BAC, AF Consultants, generated internally), address each recommendation, status and report progress on each recommendation. Our management tool report is available on the District’s web page.

Site Committee Meetings – We are advertising, and convening meetings at School sites during the evening hours in an effort to solicit public input in order to arrive at a prioritization of modernization projects. There will be sign in sheets, the meetings will be minuted.

Job Site Safety – With seven (7) projects moving into construction, we are going to be diligent in our efforts to ensure that all project participants (construction manager, trade contractors, specialty consultants) remain focused and committed to Job Site Safety. **SAFETY FIRST** is our motto, and it must be taken seriously.

1.4 Key Issues

Facilities Control System (FCS) – The financial reporting system, or budget vs. actual costs (forecast cost at completion) reporting system is being “tuned up” with input from the program manager. The revised budgets, commitments, and forecast cost to complete by phase and by project will take into account the slow down of escalation, the current bid climate, thus, deriving a more accurate projection of future scope to be completed with Proposition H, State Match and other sources of funds.

Proposition H – Implementation Plan (% of Total Need by School Site) – While we are in a position to provide a matrix (green, yellow, red light format) that will shed light on whether we have addressed the primary scopes called out for in the bond language i.e. replace aging roofs; we are not yet in a position to quantify the # of Roofs Scheduled to be Replaced (2B, 3BR, etc) vs. # of Roofs that Need to be Replaced. In other words, while a “green light” would



indicate we have replaced “aging roofs” on the buildings to be modernized, an “orange light” would indicate we are only *partially complete* in our efforts to replace all aging roofs. All of this % complete analysis will come out as a result of our upcoming budgeting efforts regarding the remaining phases.

Long Range Facilities Master Plan (Revised) – The program manager, over the course of validating the program, will be formulating a report that will provide the following: 1) Total Cost to “Modernize” all Existing Facilities to the District Standard as to “performance capabilities”. Total Cost to “Build New School” to the District Standard as to “performance capabilities”. This exercise is scheduled for completion in January 2008.

New School / 3C modernization – We are in the process of assembling information in a manner and within a prescribed timeframe so as to allow for meaningful discussions leading ultimately to making an informed decision as to how best to expend the \$65M, and any associated State Match funds derived from either course. It will be prudent to arrive at a decision as early as it permissible so as to maximize the purchasing power in terms of bricks and mortar.

Citizen’s Bond Oversight Committee – The Facilities Management department will remain committed for the duration of the implementation of Proposition H to our efforts to provide the CBOC with access to information, on paper, electronically, and visually in the form of “field visits”. We will be both proactive, and responsive to your needs, all in an effort to allow you to fulfill your obligation on behalf of the taxpayers.











2.0 Project Status Reports – “Active” Projects



MODERNIZATIONS – PHASE 1/2A





PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE			
Grossmont High School (Phase 1/2A) 	Facilities Planner: Area Program Mgr: Project Architect:	The scope of the 1A project is to upgrade the underground utilities infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) consistent with the master plan for the school site.	Phase: Completed	Budget: \$ 6,025,677	100%  <table border="1"> <tr> <td>Pre-Design</td> <td>Bid & Award</td> <td>Post-Costs</td> </tr> </table>	Pre-Design	Bid & Award	Post-Costs
Pre-Design	Bid & Award	Post-Costs						
Helix High School (Phase 1/2A) 	Facilities Planner: Area Program Mgr: Project Architect:	The scope of the 1A project is to upgrade the underground utilities infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) consistent with the master plan for the school site.	Phase: Completed	Budget: \$ 6,755,785	100%  <table border="1"> <tr> <td>Pre-Design</td> <td>Bid & Award</td> <td>Post-Costs</td> </tr> </table>	Pre-Design	Bid & Award	Post-Costs
Pre-Design	Bid & Award	Post-Costs						
El Cajon High School (Phase 1/2A) 	Facilities Planner: Area Program Mgr: Project Architect:	The scope of the 1A project is to upgrade the underground utilities infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) consistent with the master plan for the school site.	Phase: Completed	Budget: \$ 10,005,693	100%  <table border="1"> <tr> <td>Pre-Design</td> <td>Bid & Award</td> <td>Post-Costs</td> </tr> </table>	Pre-Design	Bid & Award	Post-Costs
Pre-Design	Bid & Award	Post-Costs						



Proposition H Bond Program







Progress Report – October 2007

MODERNIZATIONS – PHASE 1/2A

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE										
Mount Miguel High School (Phase 1/2A) 	Facilities Planner: Jamea Quirk Area Program Mgr: Steve Dow Project Architect:	The scope of the 1A project is to upgrade the underground utilities infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) consistent with the master plan for the school site.	Phase: Design <ul style="list-style-type: none"> <Insert Text Here> 	Budget: \$ 7,094,934	5%  <table border="1" data-bbox="641 48 695 342"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Cons</td> <td>Post-Cons</td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> </table>	Pre-Design	Design	Bid & Award	Cons	Post-Cons					
Pre-Design	Design	Bid & Award	Cons	Post-Cons											
El Capitan High School (Phase 1/2A) 	Facilities Planner: Area Program Mgr: Project Architect:	The scope of the 1A project is to upgrade the underground utilities infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) consistent with the master plan for the school site.	Phase: Completed	Budget: \$ 9,896,007	100%  <table border="1" data-bbox="1015 48 1068 342"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Cons</td> <td>Post-Cons</td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> </table>	Pre-Design	Design	Bid & Award	Cons	Post-Cons					
Pre-Design	Design	Bid & Award	Cons	Post-Cons											



MODERNIZATIONS – PHASE 1/2A

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE					
Granite Hills High School (Phase 1/2A) 	Facilities Planner: Area Program Mgr: Project Architect:	The scope of the 1A project is to upgrade the underground utilities infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) consistent with the master plan for the school site.	Phase: Completed	Budget: \$ 6,651,200	100%  <table border="1" data-bbox="634 48 691 344"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Conts</td> <td>Post-Conts</td> </tr> </table>	Pre-Design	Design	Bid & Award	Conts	Post-Conts
Pre-Design	Design	Bid & Award	Conts	Post-Conts						
Monte Vista High School (Phase 1/2A) 	Facilities Planner: Area Program Mgr: Project Architect:	The scope of the 1A project is to upgrade the underground utilities infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) consistent with the master plan for the school site.	Phase: Completed	Budget: \$ 10,270,839	100%  <table border="1" data-bbox="984 48 1040 344"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Conts</td> <td>Post-Conts</td> </tr> </table>	Pre-Design	Design	Bid & Award	Conts	Post-Conts
Pre-Design	Design	Bid & Award	Conts	Post-Conts						
Santana High School (Phase 1/2A) 	Facilities Planner: Area Program Mgr: Project Architect:	The scope of the 1A project is to upgrade the underground utilities infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) consistent with the master plan for the school site.	Phase: Completed	Budget: \$ 8,388,858	100%  <table border="1" data-bbox="1354 48 1411 344"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Conts</td> <td>Post-Conts</td> </tr> </table>	Pre-Design	Design	Bid & Award	Conts	Post-Conts
Pre-Design	Design	Bid & Award	Conts	Post-Conts						







High School District
COMPLETED BY 10/19/2010

Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 1/2A

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE					
Valhalla High School (Phase 1/2A) 	Facilities Planner: Area Program Mgr: Project Architect:	The scope of the 1A project is to upgrade the underground utilities infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) consistent with the master plan for the school site.	Phase: Completed	Budget: \$ 143,363	100%  <table border="1" data-bbox="641 52 695 346"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Award</td> <td>Cons</td> <td>Post-Cons</td> </tr> </table>	Pre-Design	Design	Award	Cons	Post-Cons
Pre-Design	Design	Award	Cons	Post-Cons						
West Hills High School (Phase 1/2A) 	Facilities Planner: Area Program Mgr: Project Architect:	The scope of the 1A project is to upgrade the underground utilities infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) consistent with the master plan for the school site.	Phase: Completed	Budget: \$ 344,496	100%  <table border="1" data-bbox="993 52 1047 346"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Award</td> <td>Cons</td> <td>Post-Cons</td> </tr> </table>	Pre-Design	Design	Award	Cons	Post-Cons
Pre-Design	Design	Award	Cons	Post-Cons						







High School District
 COMPLETED BY RESOLUTION
 87797, 12-8-1993

Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 1/2A

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE			
Steel Canyon High School (Phase 1/2A) 	Facilities Planner: Area Program Mgr: Project Architect:	The scope of the 1A project is to upgrade the underground utilities infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) consistent with the master plan for the school site.	Phase: Completed <ul style="list-style-type: none"> ADA Barriers removal. 	Budget: \$ 703,107	100%  <table border="1" data-bbox="636 50 695 344"> <tr> <td>Pre-Design</td> <td>Bid & Award</td> <td>Post-Costs</td> </tr> </table>	Pre-Design	Bid & Award	Post-Costs
Pre-Design	Bid & Award	Post-Costs						
Chaparral High School (Phase 1/2A) 	Facilities Planner: Area Program Mgr: Project Architect:	The scope of the 1A project is to upgrade the underground utilities infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) consistent with the master plan for the school site.	Phase: Completed <ul style="list-style-type: none"> Fire Alarm system, intercom, electrical upgrades & launch shelter. 	Budget: \$ 763,338	100%  <table border="1" data-bbox="1008 50 1066 344"> <tr> <td>Pre-Design</td> <td>Bid & Award</td> <td>Post-Costs</td> </tr> </table>	Pre-Design	Bid & Award	Post-Costs
Pre-Design	Bid & Award	Post-Costs						




High School District
COMMITTED TO EXCELLENCE
8110 N. G. ST. • P.O. BOX 200

Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 1/2A

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE				
<p>Work Training (Phase 1/2A)</p> <p><i>Insert Photo Here</i></p>	<p>Facilities Planner: Area Program Mgr: Project Architect: Mele Amantea</p>	<p>The scope of the 1A project is to upgrade the underground utilities infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) consistent with the master plan for the school site.</p>	<p>Phase: Completed</p> <ul style="list-style-type: none"> • ADA upgrades were performed. 	<p>Budget: \$ 479,167</p>	<p>100%</p>  <table border="1" data-bbox="613 50 669 340"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Post-Cons</td> </tr> </table>	Pre-Design	Design	Bid & Award	Post-Cons
Pre-Design	Design	Bid & Award	Post-Cons						







Grossmont Union
High School District
COMMITTED TO EXCELLENCE
EST. 1962

Proposition H Bond Program




Progress Report – October 2007

MODERNIZATIONS – PHASE 2B

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE								
Grossmont High School (Phase 2B) 	Facilities Planner: Debbie Murray Area Program Mgr: Steve Dow Project Architect: HMC Architects	The scope of the 2B project is to modernize Building(s) 500-Library, 700, and 800 consistent with the District Standards and performance capabilities within each classroom (New roof systems, HVAC, data, power, lighting) and perform all required remaining underground infrastructure (electrical, gas water, sanitary sewer, drainage, communications, fire alarm, and data). Abate all hazardous materials within the classroom buildings; address the removal of barriers consistent with the ADA transition plan.	Phase: Construction <ul style="list-style-type: none"> Building 800 is scheduled for completion by 11/15/07, however, due to fires, it will be delayed a minimum of 1 week. Moves schedules are currently being finalized. Building 700 construction will commence within next 30 days. Building 500 construction will commence by March 2008. 	Budget: \$ 8,610,344 (to be validated by PM)	21%  <table border="1"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Award</td> <td>Post-Cons</td> </tr> <tr> <td></td> <td></td> <td style="background-color: green;"></td> <td style="background-color: green;"></td> </tr> </table>	Pre-Design	Design	Award	Post-Cons				
Pre-Design	Design	Award	Post-Cons										
Helix High School (Phase 2B) 	Facilities Planner: Debbie Murray Area Program Mgr: Steve Dow Project Architect: HMC Architects	The scope of the 2B project is to modernize Building(s) 10, 100, 200, 300-Library; 800-Restroom facilities only; 1100-Restroom facilities only, 1140-Restroom facilities only, consistent with the District Standards and performance capabilities within the classroom (New roof systems, HVAC, data & power) and perform all required underground infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) work. Abate all hazardous materials within the classroom buildings; address the removal of barriers consistent with the ADA transition plan.	Phase: Construction <ul style="list-style-type: none"> Notices to Proceed have been issued to trade contractors. Flooring to be re-bid; estimated cost of \$380K included in the construction cost. 	Budget: \$ 11,290,275 (to be validated by PM)	0%  <table border="1"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Award</td> <td>Post-Cons</td> </tr> <tr> <td></td> <td></td> <td style="background-color: green;"></td> <td style="background-color: green;"></td> </tr> </table>	Pre-Design	Design	Award	Post-Cons				
Pre-Design	Design	Award	Post-Cons										







MODERNIZATIONS – PHASE 2B

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE										
<p>El Cajon Valley High School (Phase 2B)</p> 	<p>Facilities Planner: Scott Wilkins Area Program Mgr: TBD Project Architect: HMC Architects</p>	<p>The scope of the 2B project is to modernize Building(s) 100, 200, 500, consistent with the District Standards and performance capabilities within the classroom (New roof systems, HVAC, data & power) and perform all required underground infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) work. Abate all hazardous materials within the classroom buildings; address the removal of barriers consistent with the ADA transition plan.</p>	<p>Phase: Construction</p> <ul style="list-style-type: none"> Building 500 is scheduled for completion on 11/15/07, however, due to fires, it will be delayed a minimum of 1 week. Building 500 – Demolish to studs, revised scope. Building 100, 200 – Demolish to studs, revised scope. Delivery of windows is currently an issue. FF&E Budgets finalized; order placed. 	<p>Budget: \$ 9,345,175 (to be validated by PM)</p>	<p>20%</p>  <table border="1" data-bbox="657 850 747 966"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Award</td> <td>Cons</td> <td>Post-Cons</td> </tr> <tr> <td></td> <td></td> <td></td> <td style="background-color: green;"></td> <td></td> </tr> </table>	Pre-Design	Design	Award	Cons	Post-Cons					
Pre-Design	Design	Award	Cons	Post-Cons											
<p>Mount Miguel High School (Phase 2B)</p> 	<p>Facilities Planner: Janea Quirk Area Program Mgr: Steve Dow Project Architect: Mele Amantea</p>	<p>The scope of the 2B project is to modernize Building(s) 100, 200N with Library, 200S, 300N, 700E, 900, and Gym restrooms consistent with the District Standards and performance capabilities within the classroom (New roof systems, HVAC, data & power) and perform all required underground infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) work. Abate all hazardous materials within the classroom buildings; address the removal of barriers consistent with the ADA transition plan.</p>	<p>Phase: Design</p> <ul style="list-style-type: none"> Architects has commenced with the Schematic Design Phase. 	<p>Budget: \$ 9,501,183 (to be validated by PM)</p>	<p>TBD</p>										



MODERNIZATIONS – PHASE 2B





PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE								
El Capitan High School (Phase 2B) 	Facilities Planner: Dena Johnson Area Program Mgr: TBD Project Architect: HED Architects	The scope of the 2B project is to modernize Building(s) 600, 700, 800, 1000, consistent with the District Standards and performance capabilities within the classroom (New roof systems, HVAC, data & power) and perform all required underground infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) work. Abate all hazardous materials within the classroom buildings; address the removal of barriers consistent with the ADA transition plan.	Phase: Construction <ul style="list-style-type: none"> Recommendation to Award is going before the Board on November 8th. 	Budget: \$ 6,994,753 (to be validated by PM)	0%  <table border="1" data-bbox="662 48 719 346"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Post-Cons</td> </tr> <tr> <td></td> <td></td> <td style="background-color: green;"></td> <td style="background-color: green;"></td> </tr> </table>	Pre-Design	Design	Bid & Award	Post-Cons				
Pre-Design	Design	Bid & Award	Post-Cons										
Granite Hills High School (Phase 2B) 	Facilities Planner: Dena Johnson Area Program Mgr: TBD Project Architect: HMC Architects	The scope of the 2B project is to modernize Building(s) 10, 20, 40, 50, 70, 140, 160-Restroom facilities only, 230-Restroom facilities only, consistent with the District Standards and performance capabilities within the classroom (New roof systems, HVAC, data & power) and perform all required underground infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) work. Abate all hazardous materials within the classroom buildings; address the removal of barriers consistent with the ADA transition plan.	Phase: Construction <ul style="list-style-type: none"> Notices to proceed have been issued to trade contractors. 	Budget: \$ 6,628,096 (to be validated by PM)	0%  <table border="1" data-bbox="1084 48 1141 346"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Post-Cons</td> </tr> <tr> <td></td> <td></td> <td style="background-color: green;"></td> <td style="background-color: green;"></td> </tr> </table>	Pre-Design	Design	Bid & Award	Post-Cons				
Pre-Design	Design	Bid & Award	Post-Cons										



Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 2B

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE					
Monte Vista High School (Phase 2B) 	Facilities Planner: Scott Wilkins Area Program Mgr: TBD Project Architect: HED Architects	The scope of the 2B project is to modernize Building(s) 100, 200, 300, 400, Food Services, consistent with the District Standards and performance capabilities within the classroom (New roof systems, HVAC, data & power) and perform all required underground infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) work. Abate all hazardous materials within the classroom buildings; address the removal of barriers consistent with the ADA transition plan.	Phase: Bid/Award <ul style="list-style-type: none"> The bid opening was conducted on October 30th. 	Budget: \$ 7,761,073 (to be validated by PM)	50%  <table border="1" data-bbox="641 50 695 344"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Cons</td> <td>Post-Cons</td> </tr> </table>	Pre-Design	Design	Bid & Award	Cons	Post-Cons
Pre-Design	Design	Bid & Award	Cons	Post-Cons						
Santana High School (Phase 2B) 	Facilities Planner: Janea Quirk Area Program Mgr: Steve Dow Project Architect: HED Architects	The scope of the 2B project is to modernize Building(s) 100, 300, Gym Restrooms, consistent with the District Standards and performance capabilities within the classroom (New roof systems, HVAC, data & power) and perform all required underground infrastructure (electrical, gas, water, sanitary sewer, drainage, communications, fire alarm, and data) work. Abate all hazardous materials within the classroom buildings; address the removal of barriers consistent with the ADA transition plan.	Phase: Bid/Award <ul style="list-style-type: none"> The bid opening is scheduled for November 8th, delayed as a result of the wild fires. 	Budget: \$ 4,237,070 (to be validated by PM)	50%  <table border="1" data-bbox="1110 50 1164 344"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Cons</td> <td>Post-Cons</td> </tr> </table>	Pre-Design	Design	Bid & Award	Cons	Post-Cons
Pre-Design	Design	Bid & Award	Cons	Post-Cons						





Grossmont Union
High School District
COMMITTED TO EXCELLENCE
© 1997, 2007

Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 2B



PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE
Valhalla High School (Phase 2B/3A/3BR) 	Facilities Planner: Janea Quirk Area Program Mgr: Steve Dow Project Architect: Platt Whitelaw	Scope to be finalized with Platt Whitelaw this Thursday.	Phase: Design <ul style="list-style-type: none"> A design charette is scheduled for Friday, November 2nd to discuss approach to this project. 	Phase 2B: \$ 13,359,882 Phase 3A: \$ 6,860,128 <i>(combined project, budget subject to validation by program manager)</i>	TBD
West Hills High School (Phase 2B) 	Facilities Planner: Debbie Murray Area Program Mgr: Steve Dow Project Architect: HED Architects	The scope of the project encompasses repairing site drainage, irrigation, and storm systems. Upgrade fire alarm system to code. Increase electrical capacity to bring upgraded technology to all classrooms (LCD projectors, I.P. intercom system). Repair roofing drainage to prevent further damage to the campus.	Phase: Design <ul style="list-style-type: none"> Conceptual design phase has commenced. 	Budget: \$ 3,132,657 (to be validated by PM)	TBD



Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 2B

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE
<p>Chaparral High School (Phase 2B)</p> 	<p>Facilities Planner: Debbie Murray Area Program Mgr: Steve Dow Project Architect: TBD</p>	<p>The scope of the 2B project encompasses improving site ADA compliance including restroom access, remodel, path of travel. Repair and renovate existing deteriorated academic classrooms.</p>	<p>Phase: Pre-Design</p> <ul style="list-style-type: none"> Final Pre-Design phase approaching completion. 	<p>Budget: \$ 940,808 (to be validated by PM)</p>	<p>TBD</p>
<p>Steele Canyon High School (Phase 2B)</p> 	<p>Facilities Planner: Dena Johnson Area Program Mgr: TBD Project Architect: HMC Architects</p>	<p>Scope to be finalized.</p>	<p>Phase: Design</p> <ul style="list-style-type: none"> Update in the next monthly report. 	<p>Budget: \$ 618,079 (to be validated by PM)</p>	<p>TBD</p>
<p>Viking Center High School (Phase 2B)</p> <p><i>Insert Photo Here</i></p>	<p>Facilities Planner: Janea Quirk Area Program Mgr: Steve Dow Project Architect: Platt Whitelaw</p>	<p>1) Modernization of Viking Center vs. Demolish, Design and Replace Viking Center; and other programmatic solutions are currently being explored.</p>	<p>Phase: Planning</p> <ul style="list-style-type: none"> Various solutions are being explored. 	<p>Budget: \$ 1,903,386 (to be validated by PM)</p>	<p>TBD</p>



High School District
COMMITTED TO EXCELLENCE
© 1996, 2007

Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 2B

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE
Foothill Adult <i>Insert Photo Here</i>	Facilities Planner: Scott Wilkins Area Program Mgr: TBD Project Architect: TBD	The scope of this project is to install a Fire Alarm System.	Phase: TBD <ul style="list-style-type: none"> <Insert Text Here> 	Budget: \$ 457,438 (to be validated by PM)	TBD
Homestead Frontier <i>Insert Photo Here</i>	Facilities Planner: Debbie Murray Area Program Mgr: Steve Dow Project Architect: TBD	<Insert Scope Here>	Phase: TBD <ul style="list-style-type: none"> <Insert Text Here> 	Budget: \$ 0	TBD
Work Training <i>Insert Photo Here</i>	Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD		Phase: TBD <ul style="list-style-type: none"> <Insert Text Here> 	Budget: \$ 452,091 (to be validated by PM)	TBD





Grossmont Union
High School District
COMMITTED TO EXCELLENCE
817th St. • El Cajon, CA 92020

Proposition H Bond Program

Progress Report – October 2007

NEW BUILDINGS – PHASE 3A

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE										
<p>Grossmont High School (Phase 3A)</p> 	<p>Facilities Planner: Debbie Murray Area Program Mgr: Steve Dow Project Architect: HED</p>	<p>The scope of the Science Building Project (3A) encompasses designing a one story science classroom building on the site of the current boy's locker room, shower facilities and weight room. The design is approximately 14,033 GSF for the Science Building comprising eight (8) classrooms (2 Chemistry; 4 Biology; 2 Physics. If Restrooms are required, adjust SF accordingly (if applicable). The building will be designed to the current District Standards as to performance capabilities, and per Education Code and building codes (ADA compliance, Fire Life Safety, Structural). Separately, construct a new 9,250 GSF Boys Locker, Showers, Weight Room. The underground utility infrastructure (wet & dry) utilities will be removed, rerouted, installed (as required or requested) consistent with the underground utilities infrastructure plan.</p>	<p>Phase: Design</p> <ul style="list-style-type: none"> Notice to Proceed issued to HED on 10/12/07; Schematic Design – New Contract Issued: “Preliminary Construction Budget”. Schematic Design – Target Finish – November 23, 2007. 	<p>Budget: \$ 7,010,509 (to be validated by PM)</p>	<p>5%</p>  <table border="1" data-bbox="641 48 690 346"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Const</td> <td>Post-Const</td> </tr> <tr> <td></td> <td style="background-color: yellow;"></td> <td></td> <td></td> <td></td> </tr> </table>	Pre-Design	Design	Bid & Award	Const	Post-Const					
Pre-Design	Design	Bid & Award	Const	Post-Const											






High School District
 COMMITTEE TO RE-EVALUATE
 BIDDING, C, E, & P, 2006

Proposition H Bond Program



Progress Report – October 2007

NEW BUILDINGS – PHASE 3A

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE										
<p>Helix High School (Phase 3A)</p> 	<p>Facilities Planner: Debbie Murray Area Program Mgr: Steve Dow Project Architect: HED</p>	<p>The scope of the New Science Building Project (3A) encompasses designing a two-story (17,000 GSF) science classroom building. The program consists of eight (8) classrooms (2 Chemistry, 4 Biology, 2 Physics). If Restrooms are required, adjust SF accordingly (if applicable). The building will be designed to the current District Standards as to performance capabilities, and per Education Code and building codes (ADA compliance, Fire Life Safety, Structural). Site Preparation includes the demolition and removal of four (4) relocatable classrooms. The underground utility infrastructure (wet & dry) utilities will be removed, rerouted, installed (as required or requested) consistent with the underground utilities infrastructure plan.</p>	<p>Phase: Design</p> <ul style="list-style-type: none"> Notice to Proceed issued to HED on 10/12/07; Schematic Design – New Contract Issued: “Preliminary Construction Budget”. Schematic Design – Target Finish – November 23, 2007. 	<p>Budget: \$ 7,010,509 (to be validated by PM)</p>	<p>5%</p>   <table border="1" data-bbox="641 829 755 892"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Cons</td> <td>Post-Cons</td> </tr> <tr> <td></td> <td style="background-color: yellow;"></td> <td></td> <td></td> <td></td> </tr> </table>	Pre-Design	Design	Bid & Award	Cons	Post-Cons					
Pre-Design	Design	Bid & Award	Cons	Post-Cons											





NEW BUILDINGS – PHASE 3A

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE										
<p>El Cajon Valley High School (Phase 3A)</p> 	<p>Facilities Planner: Scott Wilkins Area Program Mgr: Steve Dow Project Architect: HMC Architects</p>	<p>The scope of the New Science Building Project (3A) encompasses designing a One-Story science classroom building. The design is approximately 14,033 GSF for the Science Building comprising eight (8) classrooms (2 Chemistry; 4 Biology; 2 Physics.). If Restrooms are required, adjust SF accordingly (if applicable). The building will be designed to the current District Standards as to performance capabilities, and per Education Code and building codes (ADA compliance, Fire Life Safety, Structural). The Site Preparation work includes relocating tenants from existing office space; demolish single structure; remove 3 mature trees. The underground utility infrastructure (wet & dry) utilities will be removed, rerouted, installed (as required or requested) consistent with the underground utilities infrastructure plan.</p>	<p>Phase: Design</p> <ul style="list-style-type: none"> Preliminary design is complete. 	<p>Budget: \$ 7,010,509 (to be validated by PM)</p>	<p>5%</p>  <table border="1" data-bbox="641 52 698 346"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Cons</td> <td>Post-Cons</td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> <td></td> </tr> </table>	Pre-Design	Design	Bid & Award	Cons	Post-Cons					
Pre-Design	Design	Bid & Award	Cons	Post-Cons											





NEW BUILDINGS – PHASE 3A

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE										
<p>El Capitan High School (Phase 3A)</p> 	<p>Facilities Planner: Dena Johnson Area Program Mgr: Steve Dow Project Architect: HED</p>	<p>The scope of the Science Building Project encompasses designing a One-Story science classroom building. The design is approximately 14,033 GSF for the Science Building comprising eight (8) classrooms (6 Chemistry; 2 Physics.). If Restrooms are required, adjust SF accordingly (if applicable). The building will be designed to the current District Standards as to performance capabilities, and per Education Code and building codes (ADA compliance, Fire Life Safety, Structural). The site preparation work includes the relocation of one relocatable classroom, demolition of seven (7) relocatable classrooms, demolish asphalt. The underground utility infrastructure (wet & dry) utilities will be removed, rerouted, installed (as required or requested) consistent with the underground utilities infrastructure plan.</p>	<p>Phase: Design</p> <ul style="list-style-type: none"> Notice to Proceed issued to HED on 10/12/07; Schematic Design – New Contract Issued: “Preliminary Construction Budget”. Schematic Design – Target Finish – November 23, 2007. 	<p>Budget: \$ 7,010,509 (to be validated by PM)</p>	<p>5%</p> 										
				<table border="1" data-bbox="633 819 747 966"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Const</td> <td>Post-Const</td> </tr> <tr> <td></td> <td style="background-color: yellow;"></td> <td></td> <td></td> <td></td> </tr> </table>		Pre-Design	Design	Bid & Award	Const	Post-Const					
Pre-Design	Design	Bid & Award	Const	Post-Const											



NEW BUILDINGS – PHASE 3A

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE								
<p>Granite Hills High School (Phase 3A)</p> 	<p>Facilities Planner: Dena Johnson Area Program Mgr: Steve Dow Project Architect: HMC Architects</p>	<p>The scope of the Science Building Project (3a) encompasses designing a One-Story science classroom building. The design is approximately 14,033 GSF for the Science Building comprising eight (8) classrooms (2 Chemistry; 4 Biology; 2 Physics.). If Restrooms are required, adjust SF accordingly (if applicable). The building will be designed to the current District Standards as to performance capabilities, and per Education Code and building codes (ADA compliance, Fire Life Safety, Structural). The Site preparation work consists of the relocation of one classroom; add 3 relocatable classrooms; demolition of 2 buildings, slabs, foundations. The underground utility infrastructure (wet & dry) utilities will be removed, rerouted, installed (as required or requested) consistent with the underground utilities infrastructure plan.</p>	<p>Phase: Design</p> <ul style="list-style-type: none"> Preliminary design is complete. 	<p>Budget: \$ 7,010,509 (to be validated by PM)</p>	<p>5%</p> 								
				<table border="1" data-bbox="633 819 755 892"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Post-Cons</td> </tr> <tr> <td></td> <td style="background-color: yellow;"></td> <td></td> <td></td> </tr> </table>		Pre-Design	Design	Bid & Award	Post-Cons				
Pre-Design	Design	Bid & Award	Post-Cons										





Grossmont Union
High School District
COMMITTED TO EXCELLENCE
817th St. • El Cajon, CA 92021

Proposition H Bond Program



Progress Report – October 2007

NEW BUILDINGS – PHASE 3A

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE										
<p>Monte Vista High School (Phase 3A)</p> 	<p>Facilities Planner: Scott Wilkins Area Program Mgr: Steve Dow Project Architect: HED Architects</p>	<p>The scope of the Science Building Project encompasses designing a One-Story science classroom building. The design is approximately 14,033 GSF for the Science Building comprising eight (8) classrooms (2 Chemistry; 5 Biology; 1 Physics.). The building will be designed to the current District Standards as to performance capabilities, and per Education Code and building codes (ADA compliance, Fire Life Safety, Structural). The site preparation work consists of the removal of 5 relocatables, and 2 trailers; relocate the existing "live on" trailer; relocate 2 portable classrooms. The underground utility infrastructure (wet & dry) utilities will be removed, rerouted, installed (as required or requested) consistent with the underground utilities infrastructure plan.</p>	<p>Phase: Design</p> <ul style="list-style-type: none"> Notice to Proceed issued to HED on 10/12/07; Schematic Design – New Contract Issued: "Preliminary Construction Budget". Schematic Design – Target Finish – November 23, 2007. 	<p>Budget: \$ 7,010,509 (to be validated by PM)</p>	<p>5%</p>  <table border="1" data-bbox="633 819 747 966"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Const</td> <td>Post-Const</td> </tr> <tr> <td></td> <td style="background-color: yellow;"></td> <td></td> <td></td> <td></td> </tr> </table>	Pre-Design	Design	Bid & Award	Const	Post-Const					
Pre-Design	Design	Bid & Award	Const	Post-Const											



NEW BUILDINGS – PHASE 3A




PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE										
<p>Santana High School (Phase 3A)</p> 	<p>Facilities Planner: Janea Quirk Area Program Mgr: Steve Dow Project Architect: HED Architects</p>	<p>The scope of the Science Building Project encompasses designing a One-Story science classroom building. The design is approximately 14,033 GSF for the Science Building comprising eight (8) classrooms (2 Chemistry; 4 Biology; 2 Physics.). The building will be designed to the current District Standards as to performance capabilities, and per Education Code and building codes (ADA compliance, Fire Life Safety, Structural). The Site preparation work consists of the demolition of 14 attached portables and hardscape; relocate guidance office. The underground utility infrastructure (wet & dry) utilities will be removed, rerouted, installed (as required or requested) consistent with the underground utilities infrastructure plan.</p>	<p>Phase: Design</p> <ul style="list-style-type: none"> Notice to Proceed issued to HED on 10/12/07; Schematic Design – New Contract Issued: “Preliminary Construction Budget”. Schematic Design – Target Finish – November 23, 2007. 	<p>Budget: \$ 7,010,509 (to be validated by PM)</p>	<p>5%</p>  <table border="1" data-bbox="641 829 755 976"> <tr> <td>Pre-Design</td> <td>Design</td> <td>Bid & Award</td> <td>Const</td> <td>Post-Const</td> </tr> <tr> <td></td> <td style="background-color: yellow;"></td> <td></td> <td></td> <td></td> </tr> </table>	Pre-Design	Design	Bid & Award	Const	Post-Const					
Pre-Design	Design	Bid & Award	Const	Post-Const											



Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 3BR

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE
Grossmont High School (Phase 3BR) 	Facilities Planner: Debbie Murray Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: \$ 8,114,427	TBD
Helix High School (Phase 3BR) 	Facilities Planner: Debbie Murray Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: \$ 5,368,731	TBD
El Cajon High School (Phase 3BR) 	Facilities Planner: Scott Wilkins Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: \$ 4,732,386	TBD






High School District
COMPUTERIZED BY REVIEWS, INC.
© 1997, © 1998, © 1999, © 2000

Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 3BR

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE
Mount Miguel High School (Phase 3BR) 	Facilities Planner: Janea Quirk Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: \$ 6,067,735	TBD
El Capitan High School (Phase 3BR) 	Facilities Planner: Dena Johnson Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: \$ 1,070,512	TBD
Granite Hills High School (Phase 3BR) 	Facilities Planner: Dena Johnson Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: \$ 4,581,549	TBD






High School District
 COUNTY OF LOS ANGELES
 P.O. BOX 10000
 VAN NUYS, CA 91411-0000

Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 3BR

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE
Monte Vista High School (Phase 3BR) 	Facilities Planner: Scott Wilkins Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: \$ 2,515,252	TBD
Santana High School (Phase 3BR) 	Facilities Planner: Janea Quirk Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: \$ 4,374,169	TBD
Valhalla High School (Phase 3BR) 	Facilities Planner: Janea Quirk Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: \$ 3,103,012	TBD





Grosvenor Union
High School District
COMPUTERIZED BY REVIEWSOURCE
© 1997, © 1998, © 1999, © 2000

Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 3BR

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE
West Hills High School (Phase 3BR) 	Facilities Planner: Debbie Murray Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: \$ 841,418	TBD
Steele Canyon High School (Phase 3BR) 	Facilities Planner: Dena Johnson Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: \$ 208,696	TBD
Viking Center High School (Phase 3BR) <i>Insert Photo Here</i>	Facilities Planner: Janea Quirk Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: \$ 501,267	TBD




High School District
COMPUTER TO REGISTER
8:00 AM - 8:15 PM '07

Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 3BR




PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE
Chaparral High School (Phase 3BR) 	Facilities Planner: Debbie Murray Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: \$ 260,326	TBD
Work Training (Phase 3BR) <i>Insert Photo Here</i>	Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: \$ 2,599,512	TBD
Foothills Adult (Phase 3BR) <i>Insert Photo Here</i>	Facilities Planner: Scott Wilkins Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: \$ 131,205	TBD



Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 3C

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE
<p>Grossmont High School (Phase 3C)</p> 	<p>Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD</p>	<p>TBD</p>	<p>Phase: TBD</p>	<p>Budget: TBD</p>	<p>TBD</p>
<p>Helix High School (Phase 3C)</p> 	<p>Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD</p>	<p>TBD</p>	<p>Phase: TBD</p>	<p>Budget: TBD</p>	<p>TBD</p>
<p>El Cajon High School (Phase 3C)</p> 	<p>Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD</p>	<p>TBD</p>	<p>Phase: TBD</p>	<p>Budget: TBD</p>	<p>TBD</p>






High School District
 COUNTY OF SACRAMENTO
 95701-1200

Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 3C

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE
Mount Miguel High School (Phase 3C) 	Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: TBD	TBD
El Capitan High School (Phase 3C) 	Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: TBD	TBD
Granite Hills High School (Phase 3C) 	Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: TBD	TBD






High School District
COMPUTER TO REGISTER
8:00 AM - 8:15 PM '07

Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 3C

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE
Monte Vista High School (Phase 3C) 	Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: TBD	TBD
Santana High School (Phase 3C) 	Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: TBD	TBD
Valhalla High School (Phase 3C) 	Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: TBD	TBD





High School District
COMPUTERIZED BY REGISTRATION
8 1/2" x 11" 300 DPI

Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 3C

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE
West Hills High School (Phase 3C) 	Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: TBD	TBD
Steele Canyon High School (Phase 3C) 	Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: TBD	TBD
Viking High School (Phase 3C) <i>Insert Photo Here</i>	Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: TBD	TBD




High School District
COMPUTER TO REGISTER
8:00 AM - 8:15 PM '07

Proposition H Bond Program

Progress Report – October 2007

MODERNIZATIONS – PHASE 3C

PROJECT	CONTACTS	SCOPE	PROGRESS TO DATE (PHASE)	PROJECT BUDGET	PERCENT COMPLETE
Chaparral High School (Phase 3C) 	Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: TBD	TBD
Work Training (Phase 3C) <i>Insert Photo Here</i>	Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: TBD	TBD
Foothills Adult (Phase 3C) <i>Insert Photo Here</i>	Facilities Planner: TBD Area Program Mgr: TBD Project Architect: TBD	TBD	Phase: TBD	Budget: TBD	TBD



3.0 Master Program Schedule


Activity Description	Orig Dur	% Comp	2007			2008			2009			2010			2011			2012		
			Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
GROSSMONT HS																				
1A - Infrastructure																				
+ Construction Phase	300	100	01AUG05A	31AUG06A																
2B - Modernization																				
+ Construction Phase	302	0	02JUL07A	26AUG08																
+ Close-Out Phase	22	0	27AUG08	25SEP08																
3A - New Construction																				
+ Design Phase	97	22	15OCT07A	26FEB08																
+ DSA Phase	120	0	27FEB08	12AUG08																
+ Bid / Award Phase	44	0	20AUG08	20OCT08																
+ Construction Phase	285	0	29OCT08	01DEC09																
+ Close-Out Phase	80	0	02DEC09	23MAR10																
HELIX HS																				
1A - Infrastructure																				
+ Construction Phase	300	100	01AUG05A	31AUG06A																
2B - Modernization																				
+ Construction Phase	0	0		26DEC08																
+ Close-Out Phase	86	0	29DEC08	27APR09																
3A - New Construction																				
+ Design Phase	97	4	15OCT07A	26FEB08																
+ DSA Phase	120	0	27FEB08	12AUG08																
+ Bid / Award Phase	44	0	20AUG08	20OCT08																
+ Construction Phase	285	0	29OCT08	01DEC09																
+ Close-Out Phase	86	0	02DEC09	31MAR10																



**Grossmont Unified High School District
Proposition H Bond Program
DRAFT Schedule**

Start Date: 19OCT07
 Finish Date: 28SEP10
 Data Date: 05NOV07
 Run Date: 06NOV07 08:09

Activity Description	Orig Dur	% Comp	2007			2008			2009			2010			2011			2012			
			Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
EL CAJON VALLEY HS																					
1A - Infrastructure																					
+ Construction Phase	300	100	01AUG05A	31AUG06A																	
2B - Modernization																					
+ Construction Phase	322	44	02JUL07A	23SEP08																	
+ Close-Out Phase	86	0	24SEP08	21JAN09																	
3A - New Construction																					
+ Pre-Design / Programming Phase																					
+ Design Phase	45	0	16NOV07	17JAN08																	
+ DSA Phase	80	0	18JAN08	08MAY08																	
+ Bid / Award Phase	85	0	09MAY08	04SEP08																	
+ Construction Phase	47	0	05SEP08	10NOV08																	
+ Close-Out Phase	180	0	11NOV08	20JUL09																	
+ Close-Out Phase	20	0	21JUL09	17AUG09																	
MOUNT MIGUEL HS																					
1A - Infrastructure																					
+ Pre-Design / Programming Phase																					
+ Design Phase	45	0	03DEC07	01FEB08																	
+ DSA Phase	110	0	04FEB08	04JUL08																	
+ Bid / Award Phase	205	0	07JUL08	17APR09																	
+ Construction Phase	47	0	20APR09	23JUN09																	
+ Close-Out Phase	180	0	24JUN09	02MAR10																	
+ Close-Out Phase	30	0	03MAR10	13APR10																	
2B - Modernization																					
+ Pre-Design / Programming Phase																					
+ Design Phase	45	0	05NOV07	04JAN08																	
+ Design Phase	110	0	07JAN08	06JUN08																	

Start Date 19OCT07 Finish Date 28SEP10 Data Date 05NOV07 Run Date 06NOV07 08:09	Grossmont Unified High School District Proposition H Bond Program DRAFT Schedule	 COMMITTED TO EXCELLENCE S I N C E 1 9 1 5
--	---	---


Activity Description	Orig Dur	% Comp	Early Start	Early Finish	2007			2008			2009			2010			2011			2012		
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2

GROSSMONT HS				
1A - Infrastructure				
Construction Phase				
Construction Phase	300	100	01AUG05A	31AUG06A
2B - Modernization				
Construction Phase				
Start Construction Phase	0	100	02JUL07A	26AUG08
Construction Phase	180	0	02JUL07A	26AUG08
Substantial Completion Milestone	0	0		25JUL08
Close-Out Phase				
Start Close Out Phase	0	0	27AUG08	
Punch List Items	20	0	27AUG08	23SEP08
File NOC w/ County / DSA 90 Day Letter	15	0	03SEP08	23SEP08
Final Walk Through	2	0	24SEP08	25SEP08
DSA Final Close Out	0	0		25SEP08
3A - New Construction				
Design Phase				
Start Design Phase	0	100	15OCT07A	
Schematic Design Phase	40	58	15OCT07A	27NOV07
Design Development Phase	30	0	28NOV07	08JAN08
Construction Document Phase	35	0	09JAN08	26FEB08
Design Ready for DSA Submission	0	0		26FEB08
DSA Phase				
Start DSA Phase	0	0	27FEB08	
DSA Submittal / Review Phase	100	0	27FEB08	15JUL08
Constructability Review	10	0	16JUL08	29JUL08
DSA Back Check / Approval	20	0	16JUL08	12AUG08
DSA Review Complete	0	0		12AUG08
Bid / Award Phase				
Start Bid Award Phase	0	0	20AUG08	
Prepare Bid Package	6	0	20AUG08	27AUG08
1st Advertisement	5	0	28AUG08	03SEP08
Job Walk	1	0	04SEP08	04SEP08
2nd Advertisement	5	0	05SEP08	11SEP08
Job Walk	1	0	12SEP08	12SEP08
Bid Opening	0	0		12SEP08
Protest Period / NOI Letter	5	0	15SEP08	19SEP08

Start Date	19OCT07
Finish Date	28SEP10
Data Date	05NOV07
Run Date	06NOV07 08:10

Grossmont Unified High School District
Proposition H Bond Program
DRAFT Schedule


© Primavera Systems, Inc.

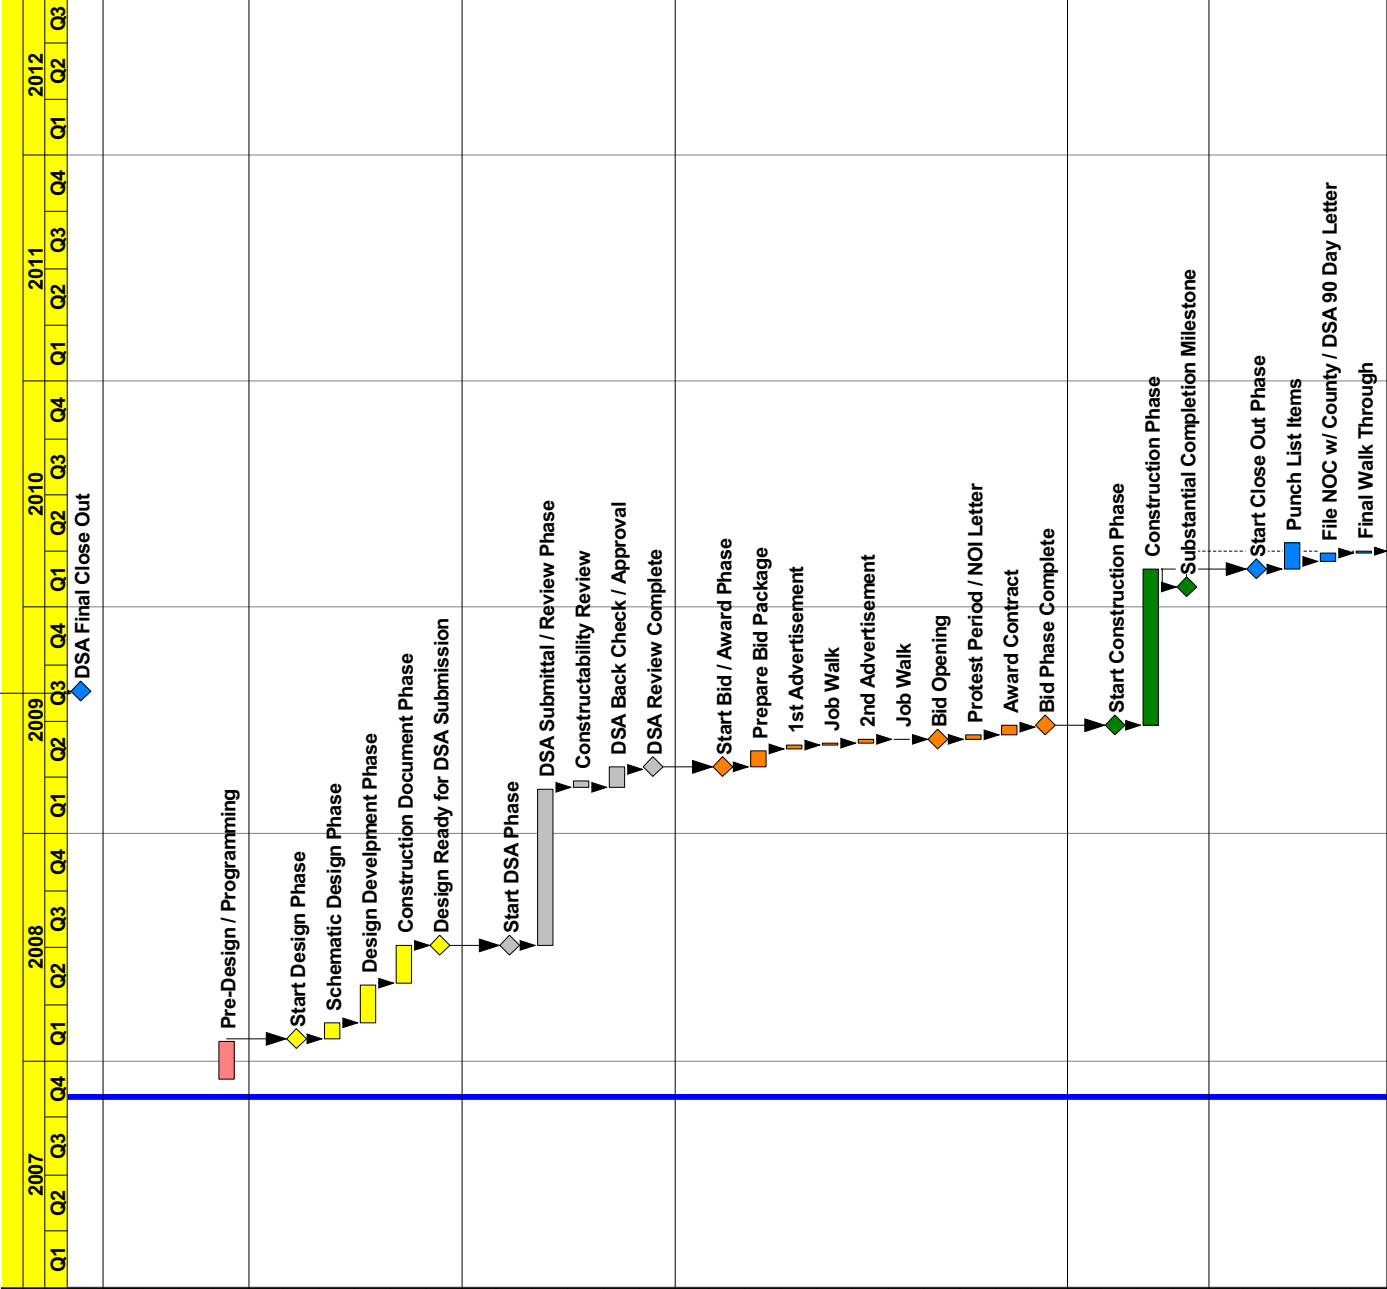

Activity Description	Orig Dur	% Comp	Early Start	Early Finish
DSA Final Close Out	0	0		17AUG09
MOUNT MIGUEL HS				
1A - Infrastructure				
Pre-Design / Programming Phase				
Pre-Design / Programming	45	0	03DEC07*	01FEB08
Design Phase				
Start Design Phase	0	0	04FEB08	
Schematic Design Phase	20	0	04FEB08	29FEB08
Design Development Phase	45	0	03MAR08	02MAY08
Construction Document Phase	45	0	05MAY08	04JUL08
Design Ready for DSA Submission	0	0		04JUL08
DSA Phase				
Start DSA Phase	0	0	07JUL08	
DSA Submittal / Review Phase	180	0	07JUL08	13MAR09
Constructability Review	10	0	16MAR09	27MAR09
DSA Back Check / Approval	25	0	16MAR09	17APR09
DSA Review Complete	0	0		17APR09
Bid / Award Phase				
Start Bid / Award Phase	0	0	20APR09	
Prepare Bid Package	20	0	20APR09	15MAY09
1st Advertisement	5	0	18MAY09	22MAY09
Job Walk	1	0	25MAY09	25MAY09
2nd Advertisement	5	0	26MAY09	01JUN09
Job Walk	1	0	02JUN09	02JUN09
Bid Opening	0	0		02JUN09
Protest Period / NOI Letter	5	0	03JUN09	09JUN09
Award Contract	10	0	10JUN09	23JUN09
Bid Phase Complete	0	0		23JUN09
Construction Phase				
Start Construction Phase	0	0	24JUN09	
Construction Phase	180	0	24JUN09	02MAR10
Substantial Completion Milestone	0	0		02FEB10
Close-Out Phase				
Start Close Out Phase	0	0	03MAR10	
Punch List Items	30	0	03MAR10	13APR10
File NOC w/ County / DSA 90 Day Letter	10	0	17MAR10	30MAR10
Final Walk Through	2	0	31MAR10	01APR10

Start Date: 19OCT07
 Finish Date: 28SEP10
 Data Date: 05NOV07
 Run Date: 06NOV07 08:11

Grossmont Unified High School District
Proposition H Bond Program
DRAFT Schedule



COMMITTED TO EXCELLENCE
 S · I · N · C · E · V · I · T · Y


© Primavera Systems, Inc.

Activity Description	Orig Dur	% Comp	Early Start	Early Finish	2007			2008			2009			2010			2011			2012		
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2

EL CAPITAN HS				
1A - Infrastructure				
Construction Phase				
Construction Phase	300	100	01AUG05A	31AUG06A
2B - Modernization				
Construction Phase				
Start Construction Phase	0	0	13NOV07*	
Construction Phase	309	0	13NOV07	16JAN09
Substantial Completion Milestone	0	0		19DEC08
Close-Out Phase				
Start Close Out Phase	0	0	19JAN09	
Punch List Items	20	0	19JAN09	13FEB09
File NOC w/ County / DSA 90 Day Letter	10	0	02FEB09	13FEB09
Final Walk Through	2	0	16FEB09	17FEB09
DSA Final Close Out	0	0		17FEB09
3A - New Construction				
Design Phase				
Start Design Phase	0	100	15OCT07A	
Schematic Design Phase	20	65	15OCT07A	13NOV07
Design Development Phase	40	0	14NOV07	08JAN08
Construction Document Phase	35	0	09JAN08	26FEB08
Design Ready for DSA Submission	0	0		26FEB08
DSA Phase				
Start DSA Phase	0	0	27FEB08	
DSA Submittal / Review Phase	100	0	27FEB08	15JUL08
Constructability Review	10	0	16JUL08	29JUL08
DSA Back Check / Approval	20	0	16JUL08	12AUG08
DSA Review Complete	0	0		12AUG08
Bid / Award Phase				
Start Bid / Award Phase	0	0	20AUG08	
Prepare Bid Package	6	0	20AUG08	27AUG08
1st Advertisement	5	0	28AUG08	03SEP08
Job Walk	1	0	04SEP08	04SEP08
2nd Advertisement	5	0	05SEP08	11SEP08
Job Walk	1	0	12SEP08	12SEP08
Bid Opening	0	0		12SEP08
Protest Period / NOI Letter	5	0	15SEP08	19SEP08

Start Date: 19OCT07
 Finish Date: 28SEP10
 Data Date: 05NOV07
 Run Date: 06NOV07 08:11


Grossmont Unified High School District
Proposition H Bond Program
DRAFT Schedule



© Primavera Systems, Inc.

Activity Description	Orig Dur	% Comp	Early Start	Early Finish	2007			2008			2009			2010			2011			2012		
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
DSA Phase																						
Start DSA Phase	0	0	09JUN08																			
DSA Submittal / Review Phase	176	0	09JUN08	09FEB09																		
Constructability Review	10	0	10FEB09	23FEB09																		
DSA Back Check / Approval	25	0	24FEB09	30MAR09																		
DSA Review Complete	0	0		30MAR09																		
Bid / Award Phase																						
Start Bid / Award Phase	0	0	31MAR09																			
Prepare Bid Package	20	0	31MAR09	27APR09																		
1st Advertisement	5	0	28APR09	04MAY09																		
Job Walk	1	0	05MAY09	05MAY09																		
2nd Advertisement	5	0	06MAY09	12MAY09																		
Job Walk	1	0	13MAY09	13MAY09																		
Bid Opening	0	0		13MAY09																		
Protest Period / NOI Letter	5	0	14MAY09	20MAY09																		
Award Contract	10	0	21MAY09	03JUN09																		
Bid Phase Complete	0	0		03JUN09																		
Construction Phase																						
Start Construction Phase	0	0	04JUN09																			
Construction Phase	180	0	04JUN09	10FEB10																		
Substantial Completion Milestone	0	0		11JAN10																		
Close-Out Phase																						
Start Close Out Phase	0	0	11FEB10																			
Punch List Items	51	0	11FEB10	22APR10																		
File NOC w/ County / DSA 90 Day Letter	30	0	23APR10	03JUN10																		
Final Walk Through	5	0	04JUN10	10JUN10																		
DSA Final Close Out	0	0		10JUN10																		
MONTE VISTA HS																						
1A - Infrastructure																						
Construction Phase	300	100	01AUG05A	31AUG06A																		
2B - Modernization																						
Construction Phase	0	0	15NOV07*																			
Construction Phase	283	0	15NOV07	15DEC08																		
Substantial Completion Milestone	0	0		17NOV08																		
<p>Start Date: 19OCT07</p> <p>Finish Date: 28SEP10</p> <p>Data Date: 05NOV07</p> <p>Run Date: 06NOV07 08:11</p>																						
<p>Grossmont Unified High School District</p> <p>Proposition H Bond Program</p> <p>DRAFT Schedule</p>																						
<p>© Primavera Systems, Inc.</p>																						

Activity Description	Orig Dur	% Comp	Early Start	Early Finish	2007			2008			2009			2010			2011			2012		
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
Close-Out Phase																						
Start Close Out Phase		0	16DEC08																			
Punch List Items	51	0	16DEC08	24FEB09																		
File NOC w/ County / DSA 90 Day Letter	30	0	25FEB09	07APR09																		
Final Walk Through	5	0	08APR09	14APR09																		
DSA Final Close Out	0	0		14APR09																		
3A - New Construction																						
Design Phase																						
Start Design Phase	0	100	15OCT07A																			
Schematic Design Phase	20	72	15OCT07A	09NOV07																		
Design Development Phase	18	0	12DEC07	04JAN08																		
Construction Document Phase	35	0	07JAN08	22FEB08																		
Design Ready for DSA Submission	0	0		22FEB08																		
DSA Phase																						
Start DSA Phase	0	0	25FEB08																			
DSA Submittal / Review Phase	100	0	25FEB08	11JUL08																		
Constructability Review	10	0	14JUL08	25JUL08																		
DSA Back Check / Approval	20	0	14JUL08	08AUG08																		
DSA Review Complete	0	0		08AUG08																		
Bid / Award Phase																						
Start Bid / Award Phase	0	0	18AUG08																			
Prepare Bid Package	6	0	18AUG08	25AUG08																		
1st Advertisement	5	0	26AUG08	01SEP08																		
Job Walk	1	0	02SEP08	02SEP08																		
2nd Advertisement	5	0	03SEP08	09SEP08																		
Job Walk	1	0	10SEP08	10SEP08																		
Bid Opening	0	0		10SEP08																		
Protest Period / NOI Letter	5	0	11SEP08	17SEP08																		
Award Contract	15	0	18SEP08	08OCT08																		
Bid Phase Complete	0	0		16OCT08																		
Construction Phase																						
Start Construction Phase	0	0	27OCT08																			
Construction Phase	285	0	27OCT08	27NOV09																		
Substantial Completion Milestone	0	0		30OCT09																		
Close-Out Phase																						
Start Close Out Phase	0	0	30NOV09																			
Punch List Items	51	0	30NOV09	08FEB10																		




**Grossmont Unified High School District
Proposition H Bond Program
DRAFT Schedule**

Start Date: 19OCT07
 Finish Date: 28SEP10
 Data Date: 05NOV07
 Run Date: 06NOV07 08:11

Activity Description	Orig Dur	% Comp	Early Start	Early Finish	2007			2008			2009			2010			2011			2012		
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
Award Contract	15	0	18SEP08	08OCT08																		
Bid Phase Complete	0	0		16OCT08																		
Construction Phase																						
Start Construction Phase	0	0	27OCT08																			
Construction Phase	285	0	27OCT08	27NOV09																		
Substantial Completion Milestone	0	0		30OCT09																		
Close-Out Phase																						
Start Close Out Phase	0	0	30NOV09																			
Punch List Items	51	0	30NOV09	08FEB10																		
File NOC w/ County / DSA 90 Day Letter	30	0	09FEB10	22MAR10																		
Final Walk Through	5	0	23MAR10	29MAR10																		
DSA Final Close Out	0	0		29MAR10																		
VALHALLA HS																						
2B - Modernization																						
Pre-Design / Programming Phase																						
Pre-Design / Programming	45	0	02JAN08*	04MAR08																		
Design Phase																						
Start Design Phase	0	0	05MAR08																			
Schematic Design Phase	20	0	05MAR08	01APR08																		
Design Development Phase	45	0	02APR08	03JUN08																		
Construction Document Phase	45	0	04JUN08	05AUG08																		
Design Ready for DSA Submission	0	0		05AUG08																		
DSA Phase																						
Start DSA Phase	0	0	06AUG08																			
DSA Submittal / Review Phase	176	0	06AUG08	08APR09																		
Constructability Review	10	0	09APR09	22APR09																		
DSA Back Check / Approval	25	0	23APR09	27MAY09																		
DSA Review Complete	0	0		27MAY09																		
Bid / Award Phase																						
Start Bid / Award Phase	0	0	28MAY09																			
Prepare Bid Package	20	0	28MAY09	24JUN09																		
1st Advertisement	5	0	25JUN09	01JUL09																		
Job Walk	1	0	02JUL09	02JUL09																		
2nd Advertisement	5	0	03JUL09	09JUL09																		
Job Walk	1	0	10JUL09	10JUL09																		
Bid Opening	0	0		10JUL09																		
Protest Period / NOI Letter	5	0	13JUL09	17JUL09																		
Start Date																						
Finish Date																						
Data Date																						
Run Date																						
19OCT07																						
28SEP10																						
05NOV07																						
06NOV07 08:11																						
Grossmont Unified High School District Proposition H Bond Program DRAFT Schedule																						
© Primavera Systems, Inc.																						


Activity Description	Orig Dur	% Comp	Early Start	Early Finish	2007			2008			2009			2010			2011			2012		
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
Construction Phase																						
Start Construction Phase	0	0	11JUN08																			
Construction Phase	181	0	11JUN08	18FEB09																		
Substantial Completion Milestone	0	0		19JAN09																		
Close-Out Phase																						
Start Close Out Phase	0	0	19FEB09																			
Punch List Items	20	0	19FEB09	18MAR09																		
File NOC w/ County / DSA 90 Day Letter	5	0	26FEB09	04MAR09																		
Final Walk Through	1	0	05MAR09	05MAR09																		
DSA Final Close Out	0	0		05MAR09																		
3A - New Construction																						
Pre-Design / Programming Phase																						
Pre-Design / Programming	45	0	05NOV07	04JAN08																		
Design Phase																						
Start Design Phase	0	0	07JAN08																			
Schematic Design Phase	20	0	07JAN08	01FEB08																		
Design Development Phase	45	0	04FEB08	04APR08																		
Construction Document Phase	45	0	07APR08	06JUN08																		
Design Ready for DSA Submission	0	0		06JUN08																		
DSA Phase																						
Start DSA Phase	0	0	09JUN08																			
DSA Submittal / Review Phase	176	0	09JUN08	09FEB09																		
Constructability Review	10	0	10FEB09	23FEB09																		
DSA Back Check / Approval	25	0	24FEB09	30MAR09																		
DSA Review Complete	0	0		30MAR09																		
Bid / Award Phase																						
Start Bid / Award Phase	0	0	31MAR09																			
Prepare Bid Package	20	0	31MAR09	27APR09																		
1st Advertisement	5	0	28APR09	04MAY09																		
Job Walk	1	0	05MAY09	05MAY09																		
2nd Advertisement	5	0	06MAY09	12MAY09																		
Job Walk	1	0	13MAY09	13MAY09																		
Bid Opening	0	0		13MAY09																		
Protest Period / NOI Letter	5	0	14MAY09	20MAY09																		
Award Contract	10	0	21MAY09	03JUN09																		
Bid Phase Complete	0	0		03JUN09																		
Start Date																						
Finish Date																						
Data Date																						
Run Date																						
19OCT07																						
28SEP10																						
05NOV07																						
06NOV07 08:11																						
Grossmont Unified High School District Proposition H Bond Program DRAFT Schedule																						
© Primavera Systems, Inc.																						

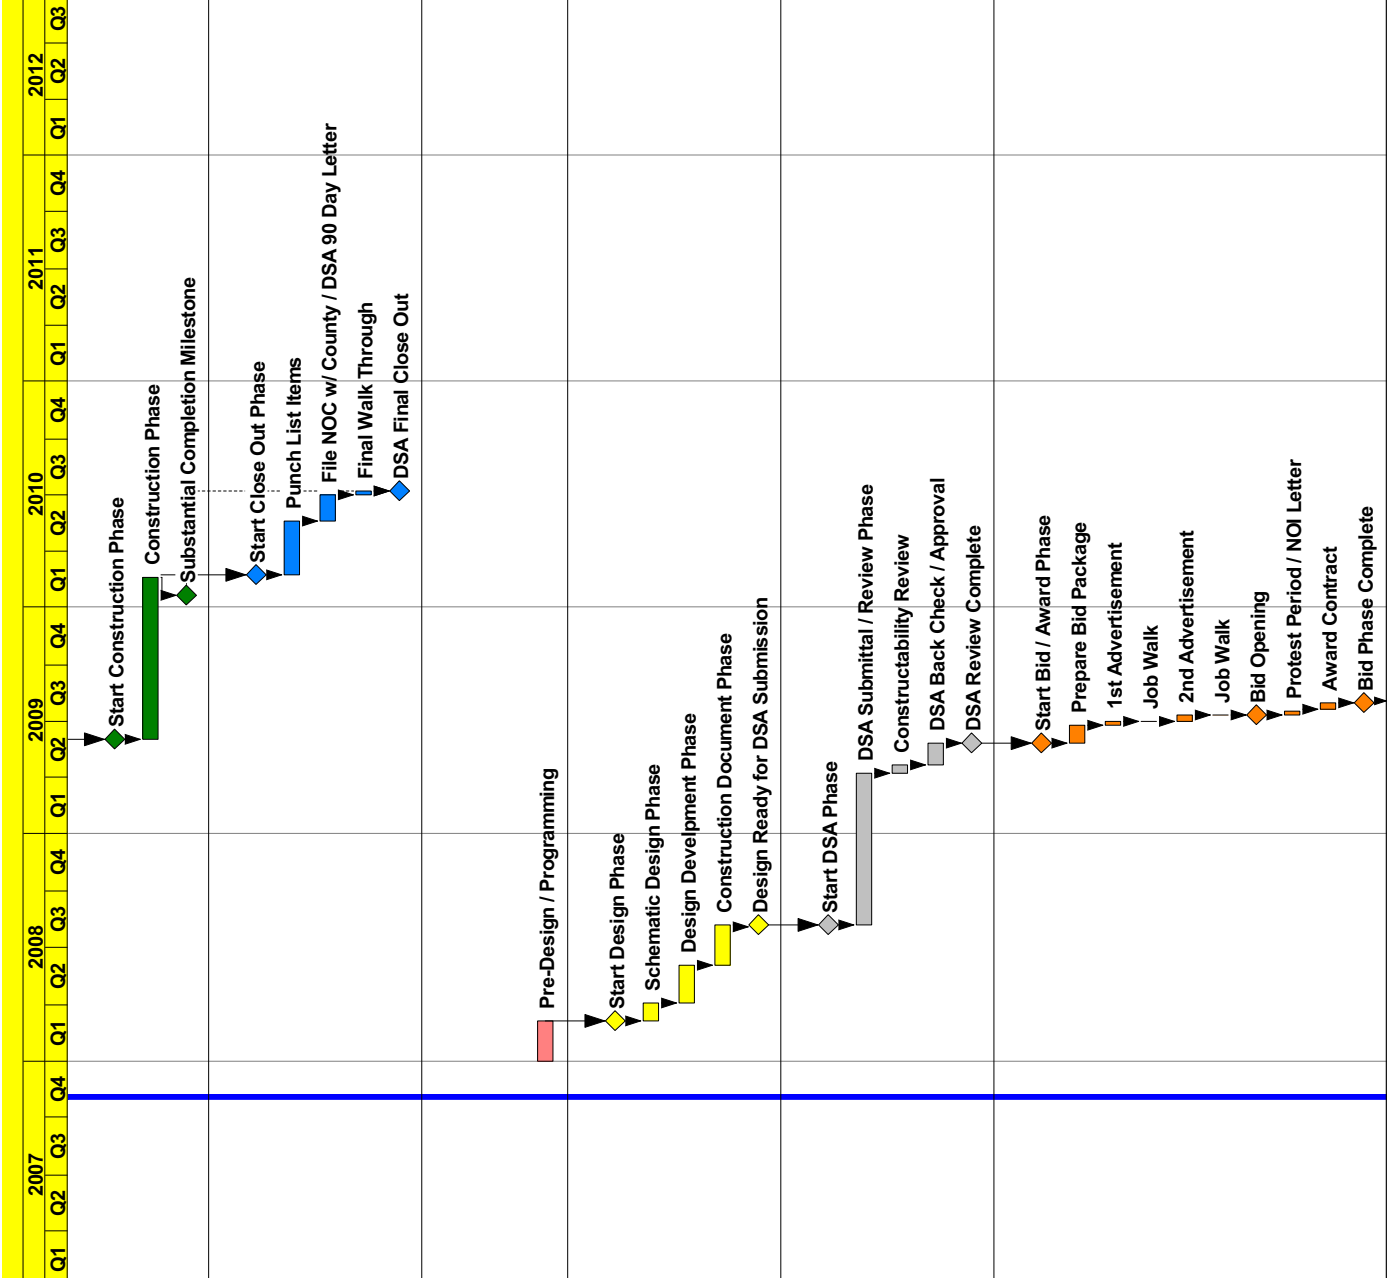

Activity Description	Orig Dur	% Comp	Early Start	Early Finish
Construction Phase				
Start Construction Phase	0	0	04JUN09	
Construction Phase	187	0	04JUN09	19FEB10
Substantial Completion Milestone	0	0		20JAN10
Close-Out Phase				
Start Close Out Phase	0	0	22FEB10	
Punch List Items	63	0	22FEB10	19MAY10
File NOC w/ County / DSA 90 Day Letter	30	0	20MAY10	30JUN10
Final Walk Through	5	0	01JUL10	07JUL10
DSA Final Close Out	0	0		07JUL10
STEELE CANYON HS				
2B - Modernization				
Pre-Design / Programming Phase				
Pre-Design / Programming	45	0	02JAN08*	04MAR08
Design Phase				
Start Design Phase	0	0	05MAR08	
Schematic Design Phase	20	0	05MAR08	01APR08
Design Development Phase	45	0	02APR08	03JUN08
Construction Document Phase	45	0	04JUN08	05AUG08
Design Ready for DSA Submission	0	0		05AUG08
DSA Phase				
Start DSA Phase	0	0	06AUG08	
DSA Submittal / Review Phase	176	0	06AUG08	08APR09
Constructability Review	10	0	09APR09	22APR09
DSA Back Check / Approval	25	0	23APR09	27MAY09
DSA Review Complete	0	0		27MAY09
Bid / Award Phase				
Start Bid / Award Phase	0	0	28MAY09	
Prepare Bid Package	20	0	28MAY09	24JUN09
1st Advertisement	5	0	25JUN09	01JUL09
Job Walk	1	0	02JUL09	02JUL09
2nd Advertisement	5	0	03JUL09	09JUL09
Job Walk	1	0	10JUL09	10JUL09
Bid Opening	0	0		10JUL09
Protest Period / NOI Letter	5	0	13JUL09	17JUL09
Award Contract	10	0	20JUL09	31JUL09
Bid Phase Complete	0	0		31JUL09

Start Date: 19OCT07
 Finish Date: 28SEP10
 Data Date: 05NOV07
 Run Date: 06NOV07 08:11

Grossmont Unified High School District
Proposition H Bond Program
DRAFT Schedule



High School District
 COMMITTED TO EXCELLENCE
 S I N C E 1 9 1 5


© Primavera Systems, Inc.

Activity Description	Orig Dur	% Comp	2007		2008				2009				2010				2011				2012							
			Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4		
Construction Phase																												
Start Construction Phase	0	0																										
Construction Phase	187	0	03AUG09																									
Substantial Completion Milestone	0	0																										
Close-Out Phase																												
Start Close Out Phase	0	0	21APR10																									
Punch List Items	63	0	21APR10																									
File NOC w/ County / DSA 90 Day Letter	30	0	19JUL10																									
Final Walk Through	5	0	30AUG10																									
DSA Final Close Out	0	0																										
3A - New Construction																												
Pre-Design / Programming Phase																												
Pre-Design / Programming	45	0	02JAN08*																									
Design Phase																												
Start Design Phase	0	0	05MAR08																									
Schematic Design Phase	20	0	05MAR08																									
Design Development Phase	45	0	02APR08																									
Construction Document Phase	45	0	04JUN08																									
Design Ready for DSA Submission	0	0																										
DSA Phase																												
Start DSA Phase	0	0	06AUG08																									
DSA Submittal / Review Phase	176	0	06AUG08																									
Constructability Review	10	0	09APR09																									
DSA Back Check / Approval	25	0	23APR09																									
DSA Review Complete	0	0																										
Bid / Award Phase																												
Start Bid / Award Phase	0	0	28MAY09																									
Prepare Bid Package	20	0	28MAY09																									
1st Advertisement	5	0	25JUN09																									
Job Walk	1	0	02JUL09																									
2nd Advertisement	5	0	03JUL09																									
Job Walk	1	0	10JUL09																									
Bid Opening	0	0																										
Protest Period / NOI Letter	5	0	13JUL09																									
Award Contract	10	0	20JUL09																									
Bid Phase Complete	0	0																										



**Grossmont Unified High School District
Proposition H Bond Program
DRAFT Schedule**

Start Date 19OCT07
 Finish Date 28SEP10
 Data Date 05NOV07
 Run Date 06NOV07 08:11

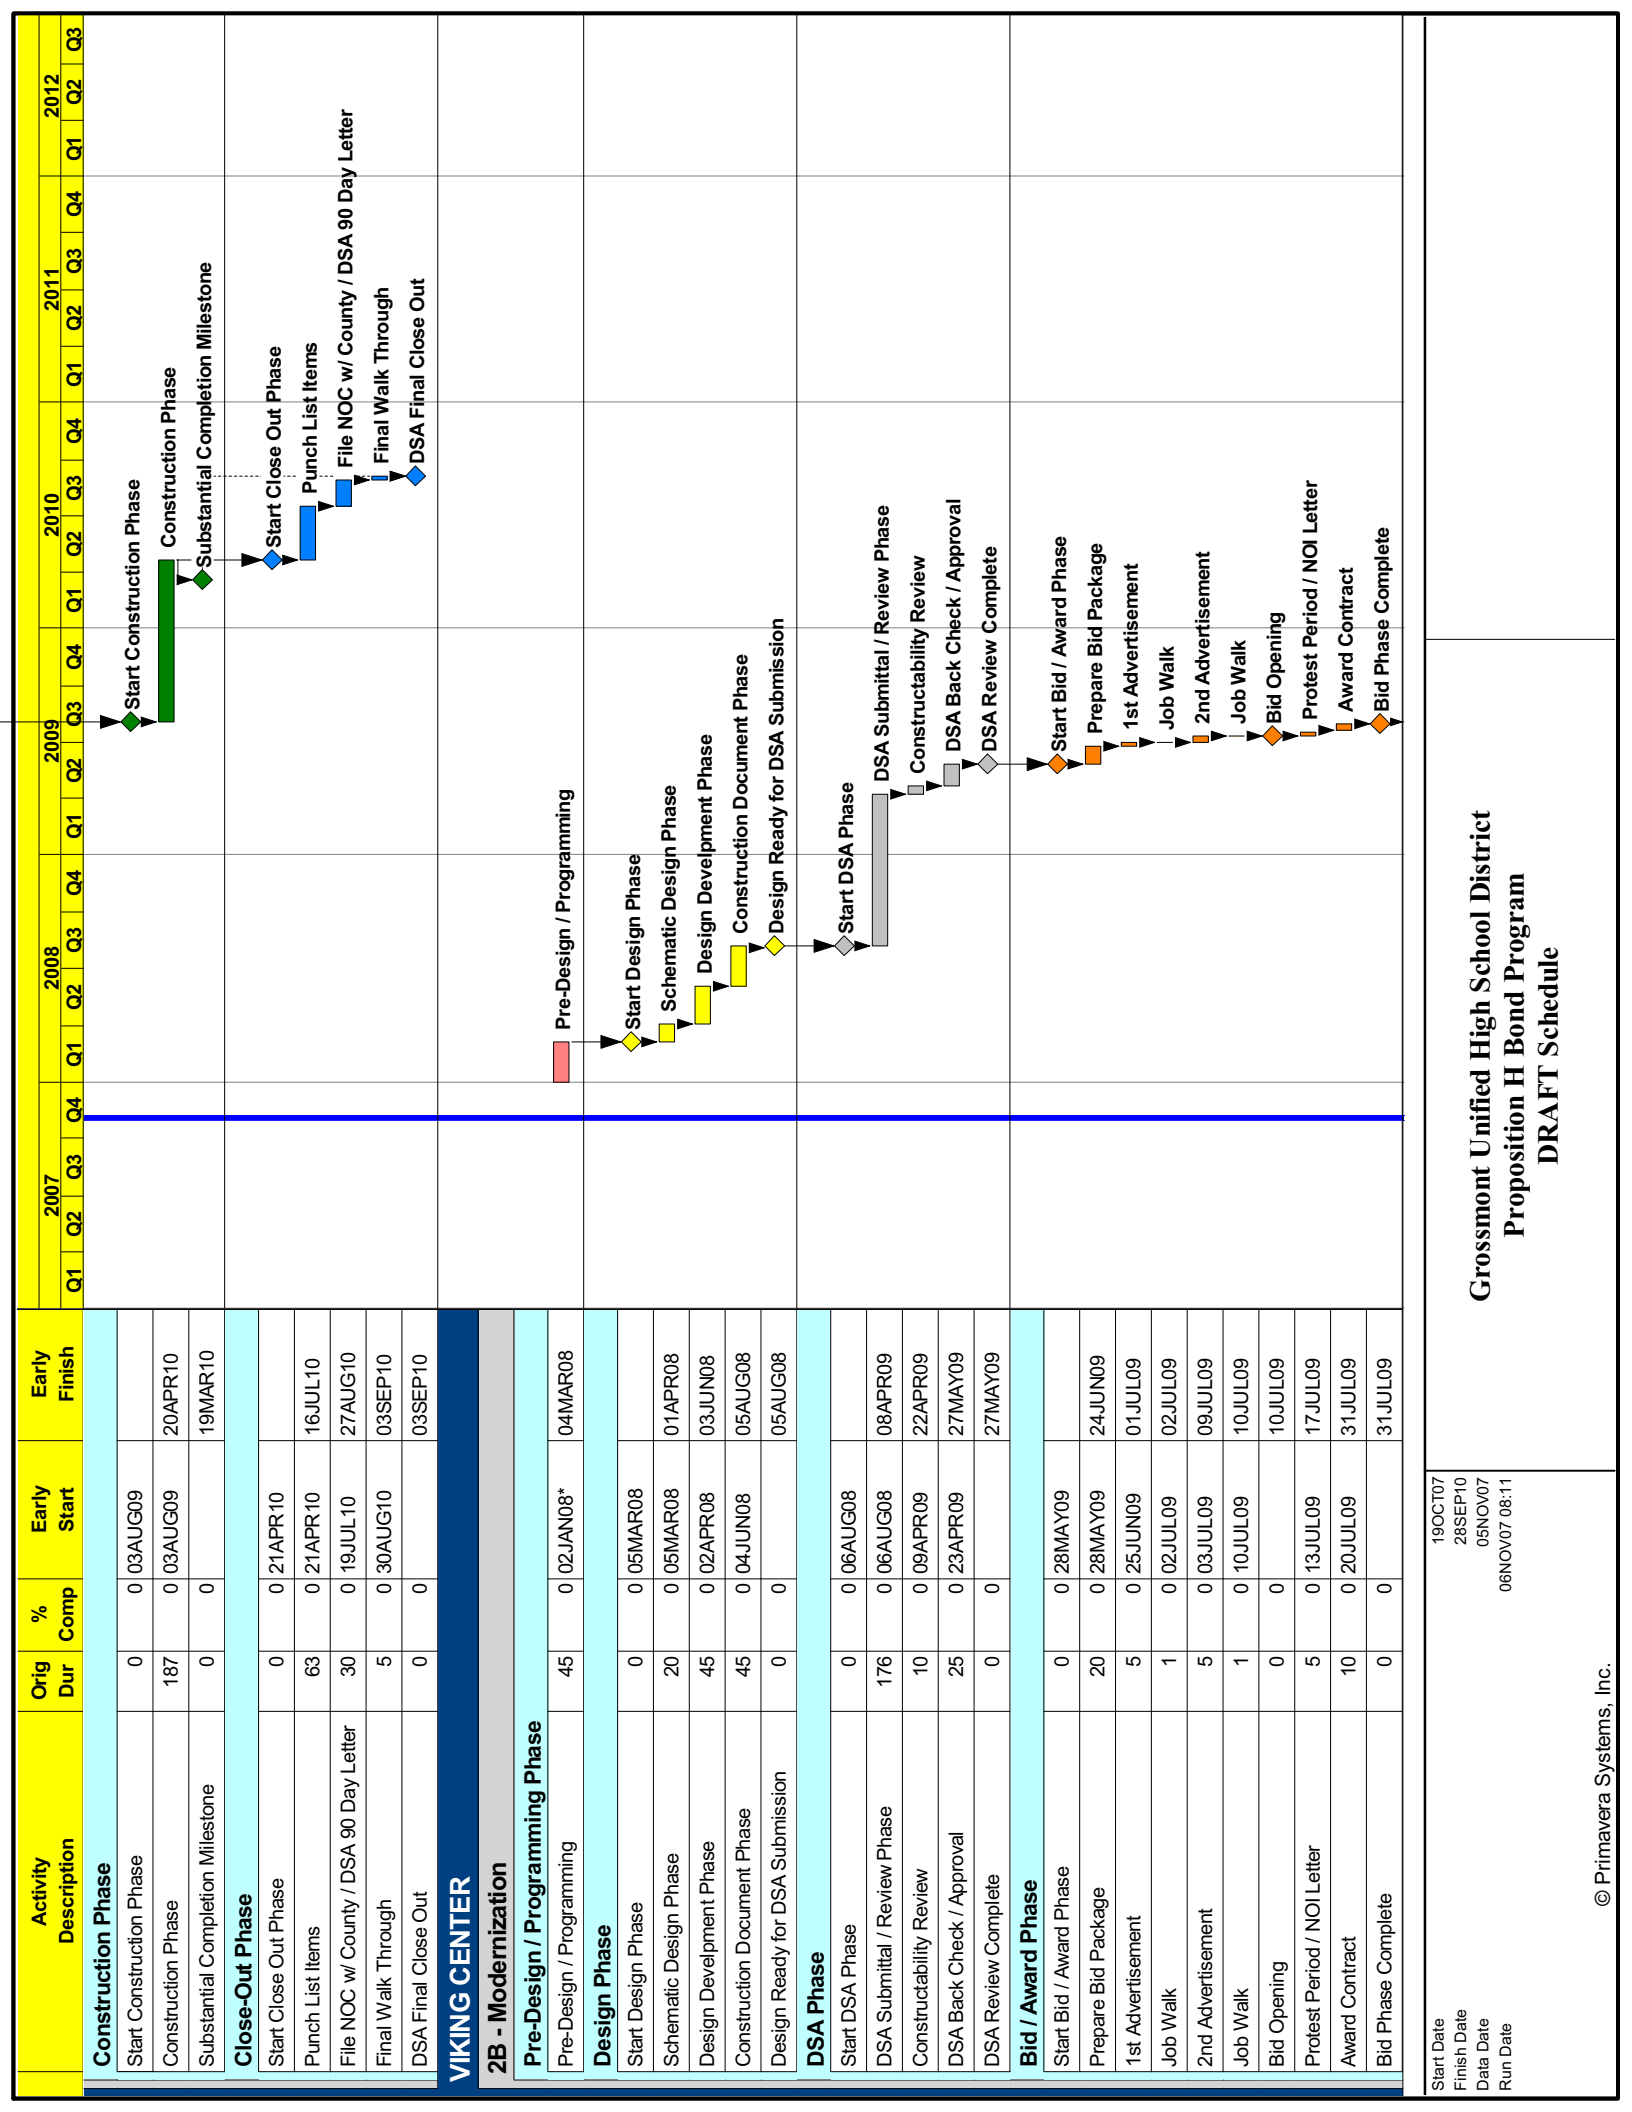


Activity Description	Orig Dur	% Comp	2007			2008			2009			2010			2011			2012		
			Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2

Activity Description	Orig Dur	% Comp	Early Start	Early Finish
Construction Phase				
Start Construction Phase	0	0	03AUG09	
Construction Phase	187	0	03AUG09	20APR10
Substantial Completion Milestone	0	0		19MAR10
Close-Out Phase				
Start Close Out Phase	0	0	21APR10	
Punch List Items	63	0	21APR10	16JUL10
File NOC w/ County / DSA 90 Day Letter	30	0	19JUL10	27AUG10
Final Walk Through	5	0	30AUG10	03SEP10
DSA Final Close Out	0	0		03SEP10
VIKING CENTER				
2B - Modernization				
Pre-Design / Programming Phase				
Pre-Design / Programming	45	0	02JAN08*	04MAR08
Design Phase				
Start Design Phase	0	0	05MAR08	
Schematic Design Phase	20	0	05MAR08	01APR08
Design Development Phase	45	0	02APR08	03JUN08
Construction Document Phase	45	0	04JUN08	05AUG08
Design Ready for DSA Submission	0	0		05AUG08
DSA Phase				
Start DSA Phase	0	0	06AUG08	
DSA Submittal / Review Phase	176	0	06AUG08	08APR09
Constructability Review	10	0	09APR09	22APR09
DSA Back Check / Approval	25	0	23APR09	27MAY09
DSA Review Complete	0	0		27MAY09
Bid / Award Phase				
Start Bid / Award Phase	0	0	28MAY09	
Prepare Bid Package	20	0	28MAY09	24JUN09
1st Advertisement	5	0	25JUN09	01JUL09
Job Walk	1	0	02JUL09	02JUL09
2nd Advertisement	5	0	03JUL09	09JUL09
Job Walk	1	0	10JUL09	10JUL09
Bid Opening	0	0		10JUL09
Protest Period / NOI Letter	5	0	13JUL09	17JUL09
Award Contract	10	0	20JUL09	31JUL09
Bid Phase Complete	0	0		31JUL09

Activity Description	Orig Dur	% Comp	Early Start	Early Finish
Start Date			19OCT07	
Finish Date			28SEP10	
Data Date			05NOV07	
Run Date			06NOV07 08:11	


**Grossmont Unified High School District
Proposition H Bond Program
DRAFT Schedule**

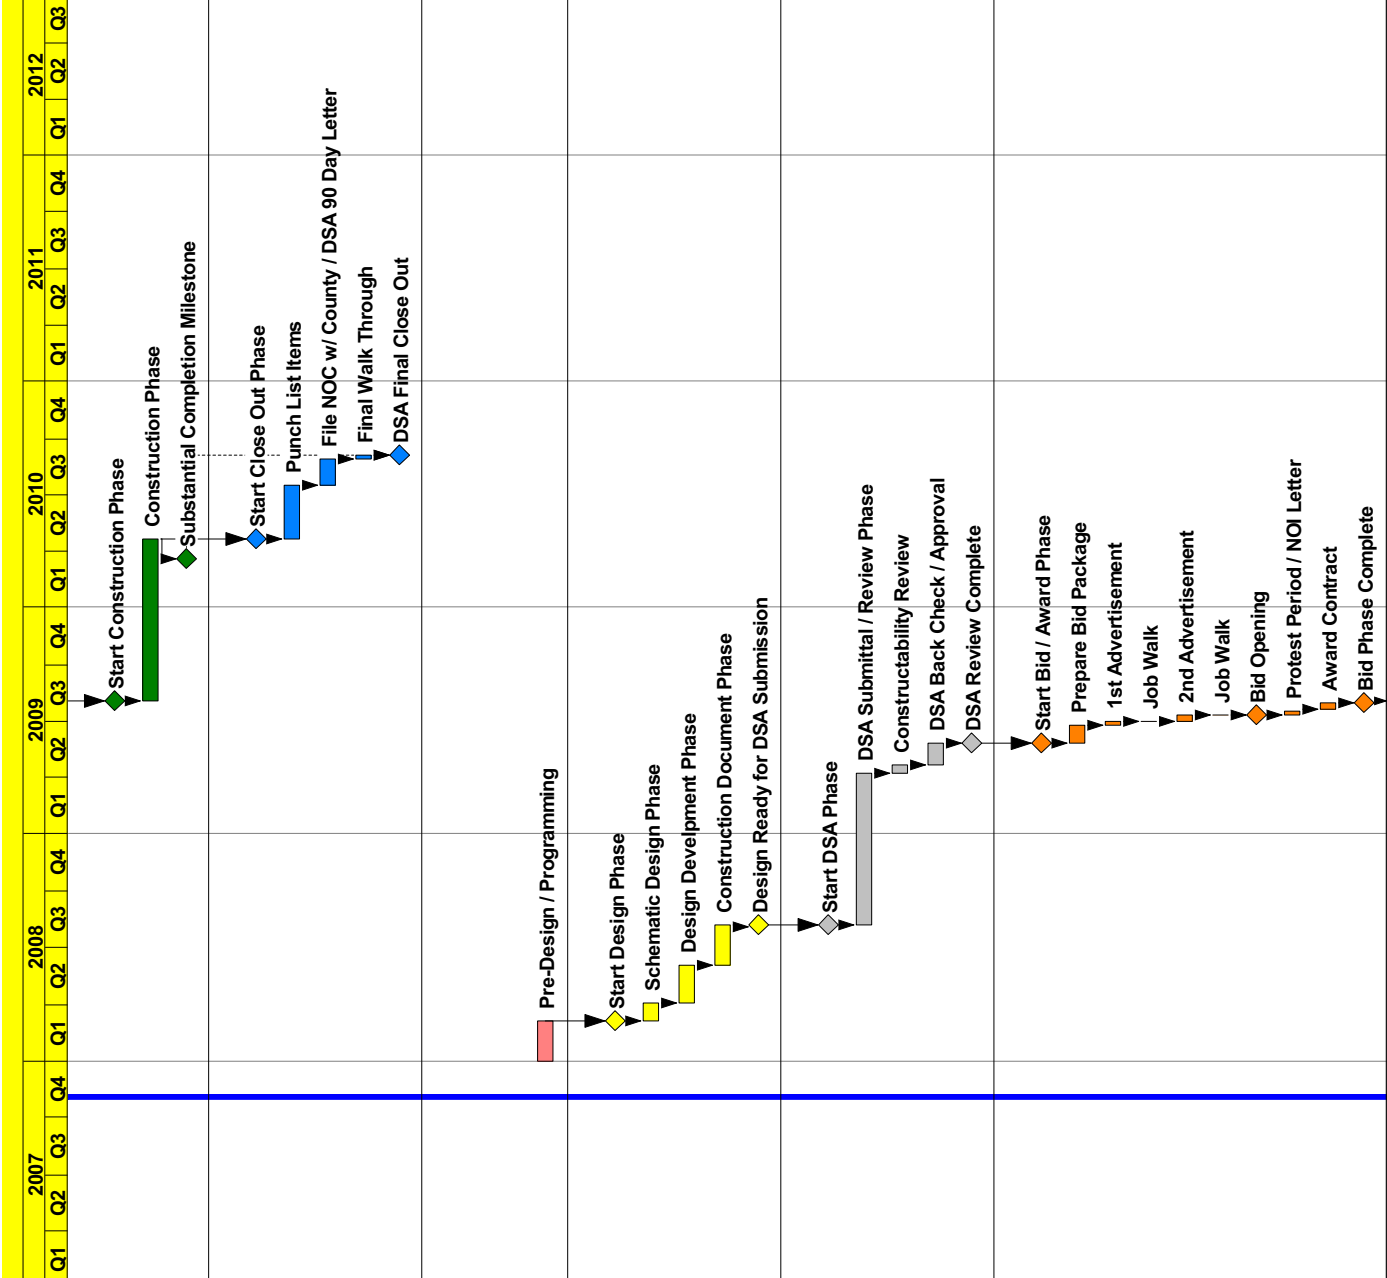

Activity Description	Orig Dur	% Comp	Early Start	Early Finish
Construction Phase				
Start Construction Phase	0	0	03AUG09	
Construction Phase	187	0	03AUG09	20APR10
Substantial Completion Milestone	0	0		19MAR10
Close-Out Phase				
Start Close Out Phase	0	0	21APR10	
Punch List Items	63	0	21APR10	16JUL10
File NOC w/ County / DSA 90 Day Letter	30	0	19JUL10	27AUG10
Final Walk Through	5	0	30AUG10	03SEP10
DSA Final Close Out	0	0		03SEP10
FOOTBALL ADULT				
2B - Modernization				
Pre-Design / Programming Phase				
Pre-Design / Programming	45	0	02JAN08*	04MAR08
Design Phase				
Start Design Phase	0	0	05MAR08	
Schematic Design Phase	20	0	05MAR08	01APR08
Design Development Phase	45	0	02APR08	03JUN08
Construction Document Phase	45	0	04JUN08	05AUG08
Design Ready for DSA Submission	0	0		05AUG08
DSA Phase				
Start DSA Phase	0	0	06AUG08	
DSA Submittal / Review Phase	176	0	06AUG08	08APR09
Constructability Review	10	0	09APR09	22APR09
DSA Back Check / Approval	25	0	23APR09	27MAY09
DSA Review Complete	0	0		27MAY09
Bid / Award Phase				
Start Bid / Award Phase	0	0	28MAY09	
Prepare Bid Package	20	0	28MAY09	24JUN09
1st Advertisement	5	0	25JUN09	01JUL09
Job Walk	1	0	02JUL09	02JUL09
2nd Advertisement	5	0	03JUL09	09JUL09
Job Walk	1	0	10JUL09	10JUL09
Bid Opening	0	0		10JUL09
Protest Period / NOI Letter	5	0	13JUL09	17JUL09
Award Contract	10	0	20JUL09	31JUL09
Bid Phase Complete	0	0		31JUL09

Start Date: 19OCT07
 Finish Date: 28SEP10
 Data Date: 05NOV07
 Run Date: 06NOV07 08:11

Grossmont Unified High School District
Proposition H Bond Program
DRAFT Schedule



COMMITTED TO EXCELLENCE
 S · I · N · C · E · I · T · Y


© Primavera Systems, Inc.

Activity Description	Orig Dur	% Comp	2007				2008				2009				2010				2011				2012								
			Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4					
Construction Phase																															
Start Construction Phase	0	0	03AUG09																												
Construction Phase	187	0	03AUG09																												
Substantial Completion Milestone	0	0																													
Close-Out Phase																															
Start Close Out Phase	0	0	21APR10																												
Punch List Items	63	0	21APR10																												
File NOC w/ County / DSA 90 Day Letter	30	0	19JUL10																												
Final Walk Through	5	0	30AUG10																												
DSA Final Close Out	0	0																													
HOMESTEAD FRONTIER																															
2B - Modernization																															
Design Phase																															
Start Design Phase	0	0	02JUL08*																												
Schematic Design Phase	20	0	02JUL08																												
Design Development Phase	20	0	30JUL08																												
Construction Document Phase	25	0	27AUG08																												
Design Ready for DSA Submission	0	0																													
DSA Phase																															
Start DSA Phase	0	0	01OCT08																												
DSA Submittal / Review Phase	140	0	01OCT08																												
Constructability Review	7	0	15APR09																												
DSA Back Check / Approval	17	0	22APR09																												
DSA Review Complete	0	0																													
Bid / Award Phase																															
Start Bid / Award Phase	0	0	15MAY09																												
Prepare Bid Package	20	0	15MAY09																												
1st Advertisement	5	0	12JUN09																												
Job Walk	1	0	19JUN09																												
2nd Advertisement	5	0	22JUN09																												
Job Walk	1	0	29JUN09																												
Bid Opening	0	0																													
Protest Period / NOI Letter	5	0	30JUN09																												
Award Contract	15	0	07JUL09																												
Bid Phase Complete	0	0																													
Construction Phase																															
Start Construction Phase	0	0	30JUL09																												

Start Date: 19OCT07
 Finish Date: 28SEP10
 Data Date: 05NOV07
 Run Date: 06NOV07 08:11


© Primavera Systems, Inc.

Grossmont Unified High School District Proposition H Bond Program DRAFT Schedule



COMMITTED TO EXCELLENCE
 S · I · N · C · E · V · I · T · Y

Activity Description	2007				2008				2009				2010				2011				2012			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Construction Phase																								
Substantial Completion Milestone																								
Close-Out Phase																								
Start Close Out Phase																								
Punch List Items																								
File NOC w/ County / DSA 90 Day Letter																								
Final Walk Through																								
DSA Final Close Out																								



Start Date	19OCT07
Finish Date	28SEP10
Data Date	05NOV07
Run Date	06NOV07 08:11

Grossmont Unified High School District Proposition H Bond Program DRAFT Schedule	
---	--

© Primavera Systems, Inc.	
---------------------------	--




4.0 Financial (*future*)

(next report)




5.0 Statistical Data

GUHSD Prop H* Expenditure Plan by Fiscal Year (Program to date through 09/30/07)

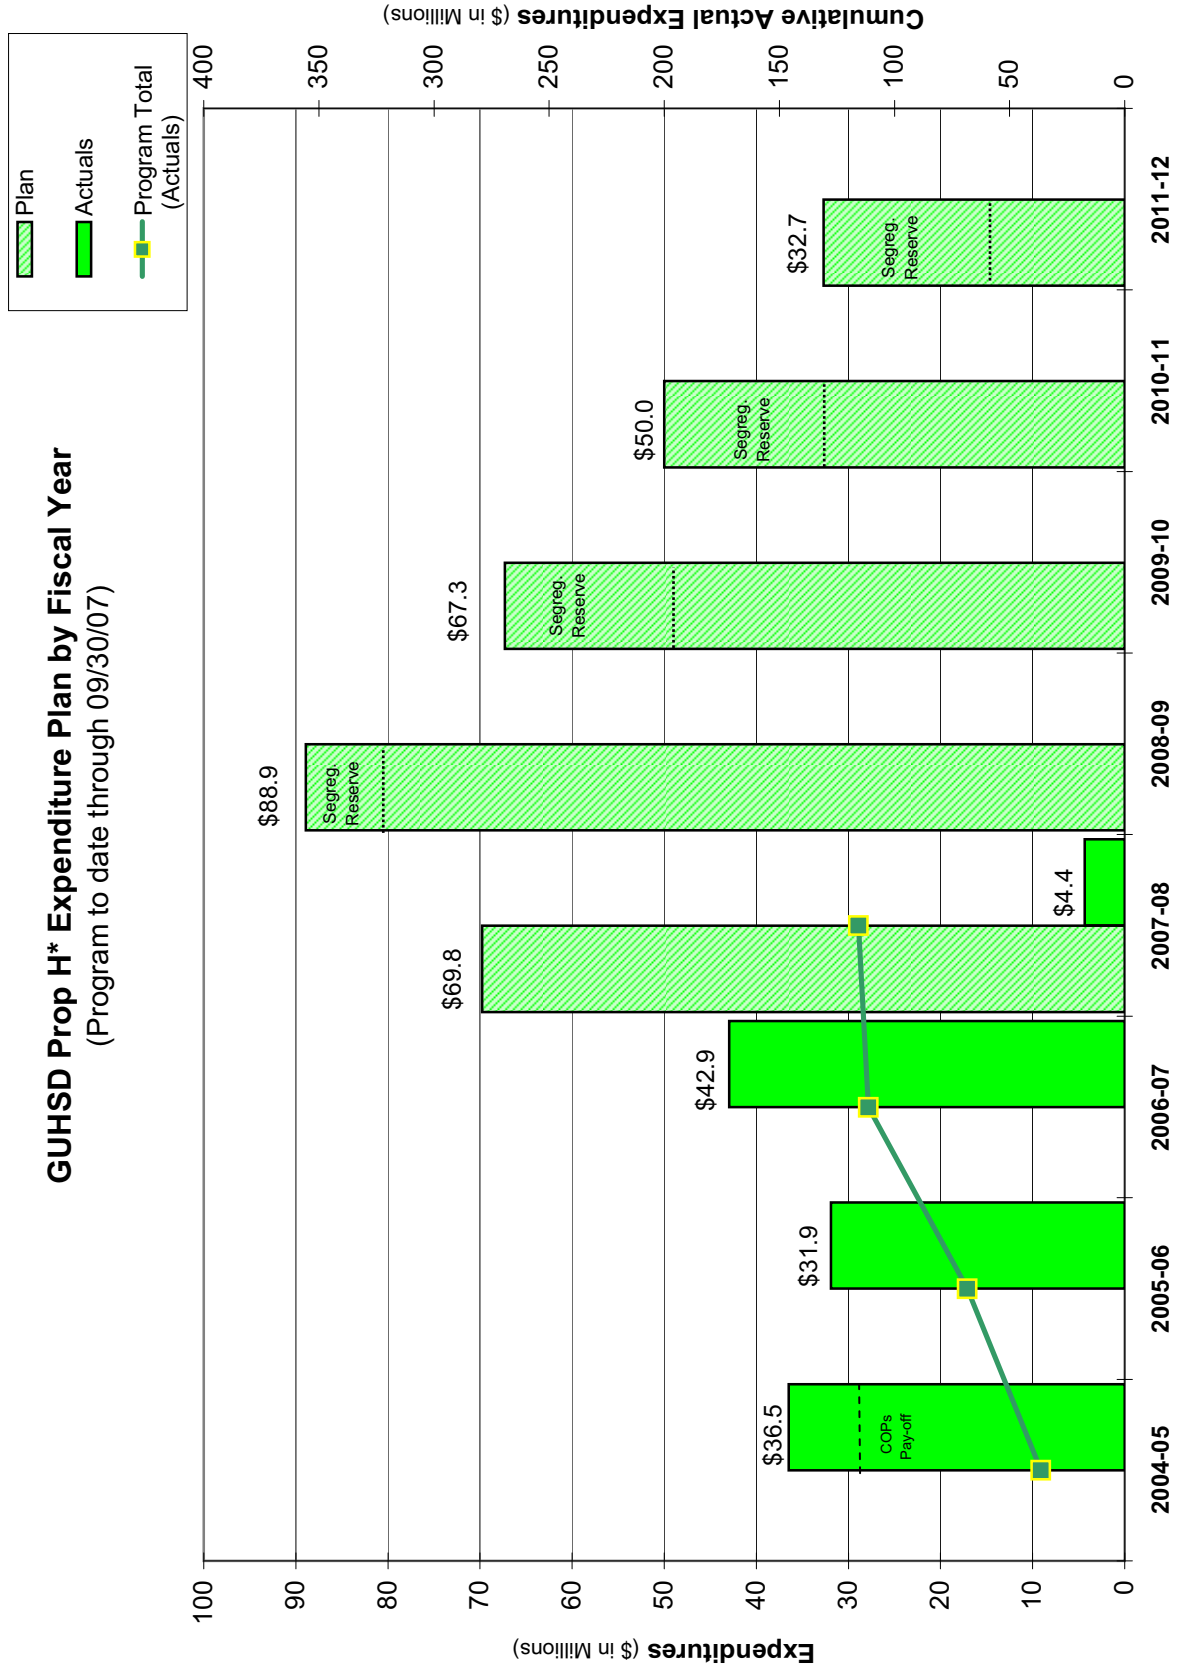


GUHSD PROP H* Expenditures by Month
 Fiscal Year 2007-08 Year-to-Date 09/30/07

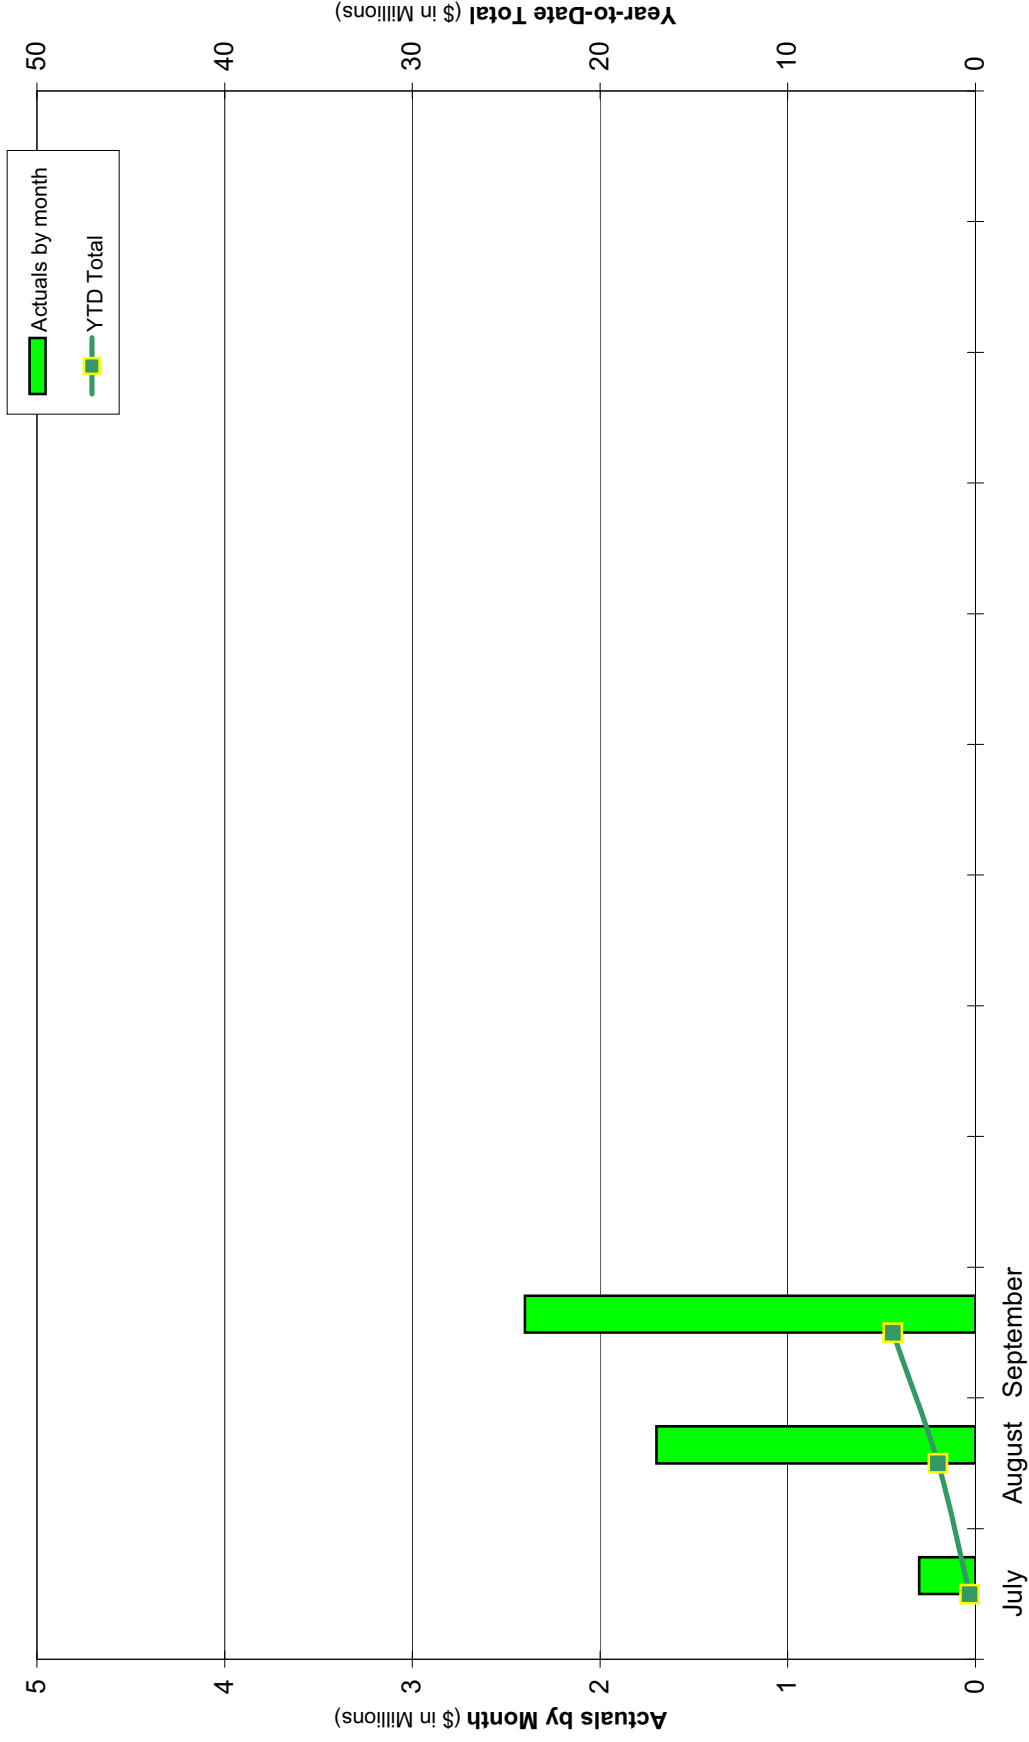


*Includes State School Facility Program Matching Funds

GUHSD PROP H* Expenditures vs. Available Cash
 Fiscal Year 2007-08 Year-to-Date 09/30/07

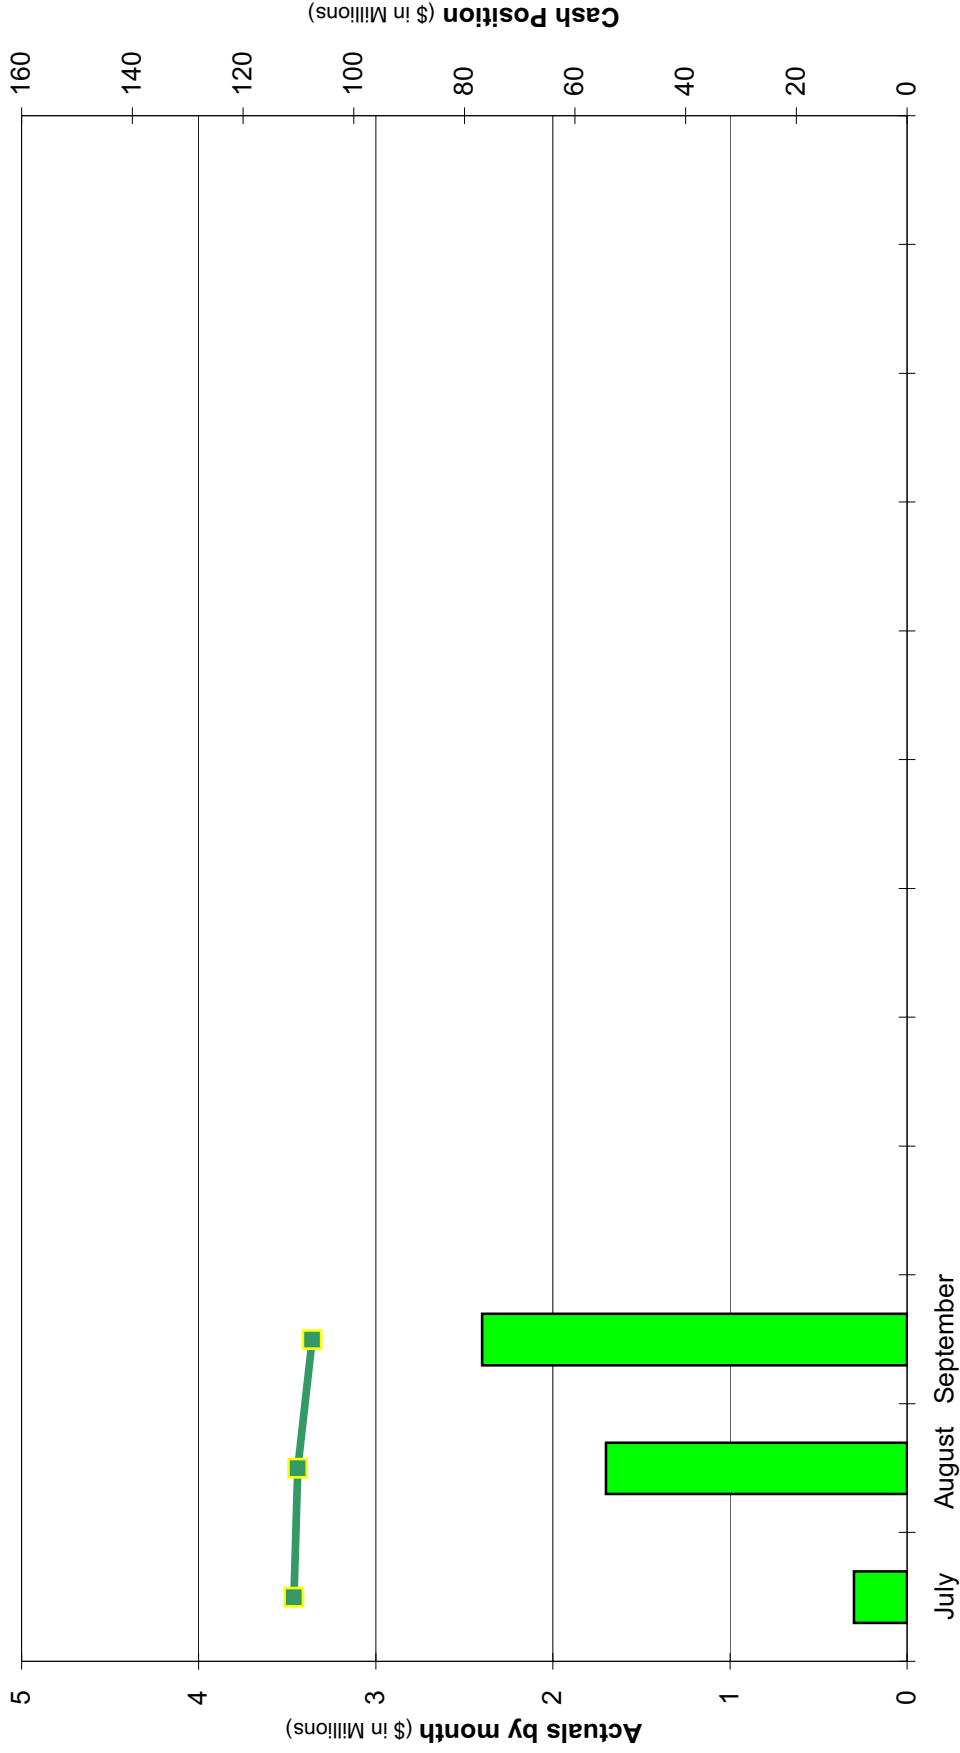

*Includes State School Facility Program Matching Funds


GUHSD PROP H* Actual Expenditures by Type
 (Program to date through 09/30/07) Total \$115.7M

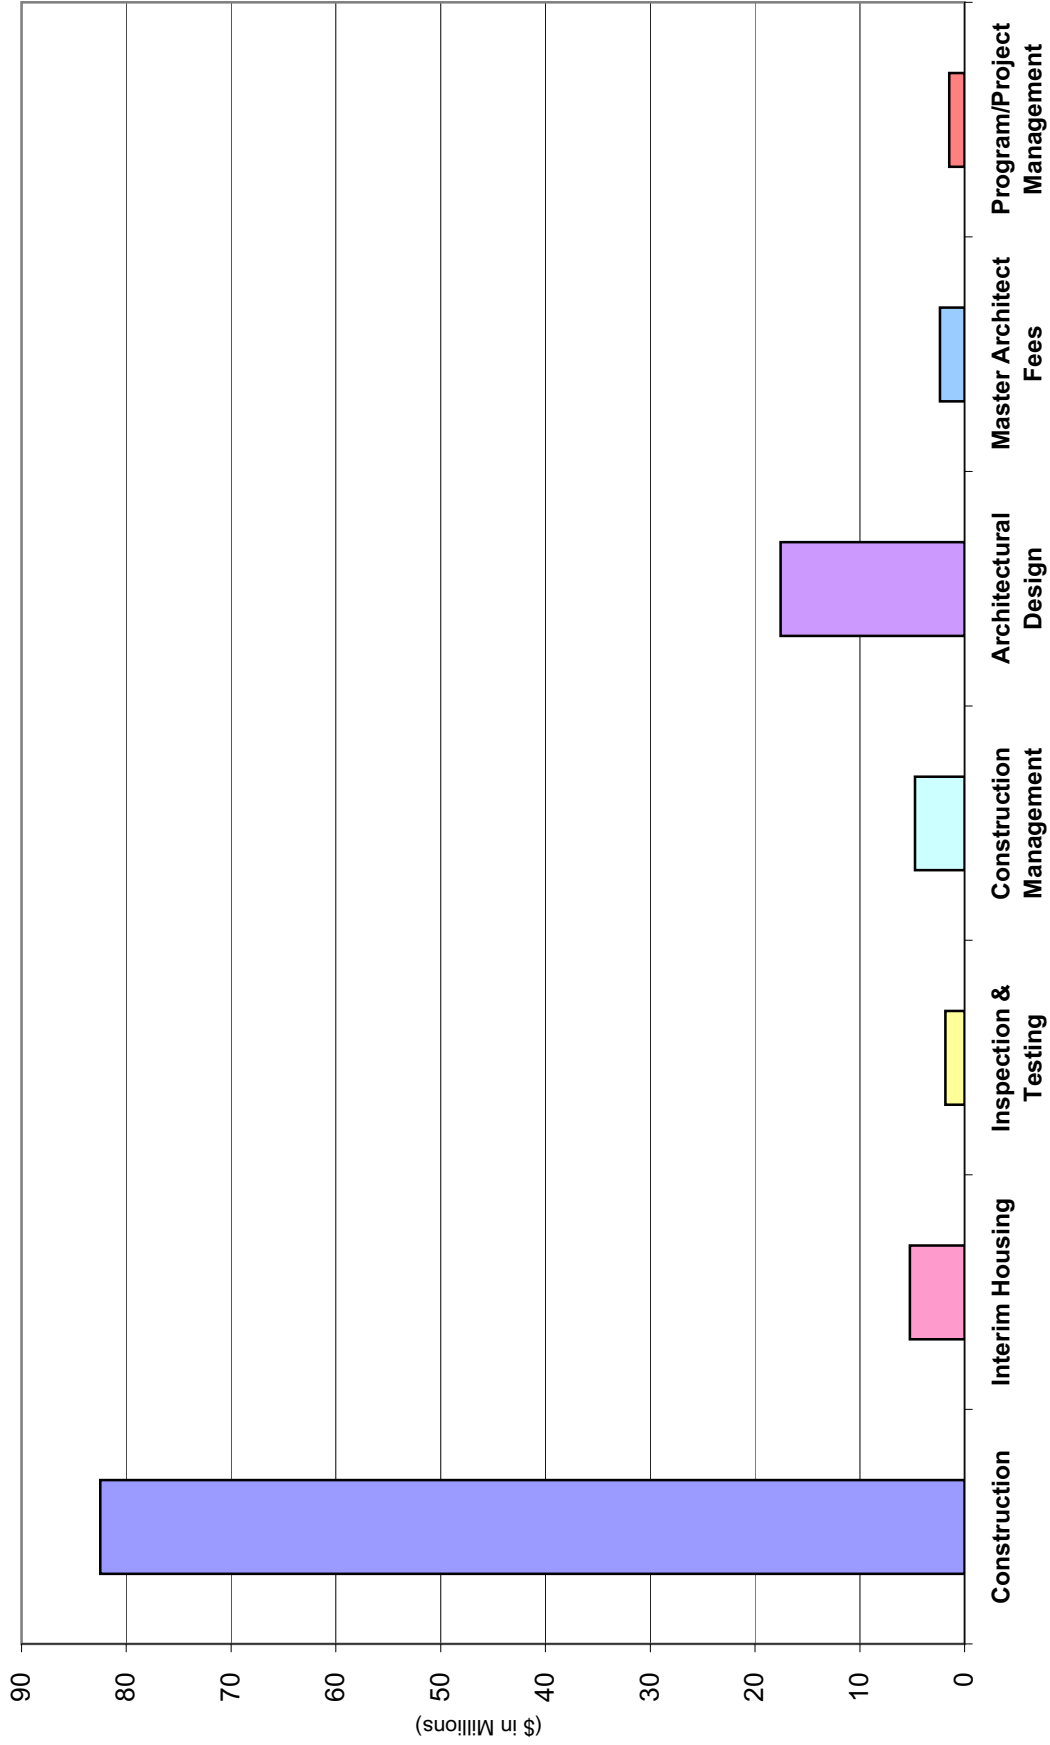

*Includes State School Facility Program Matching Funds


GUHSD PROP H* Actual Expenditures by Type Excluding Construction

(Program to date through 09/30/07) Total \$33.2M

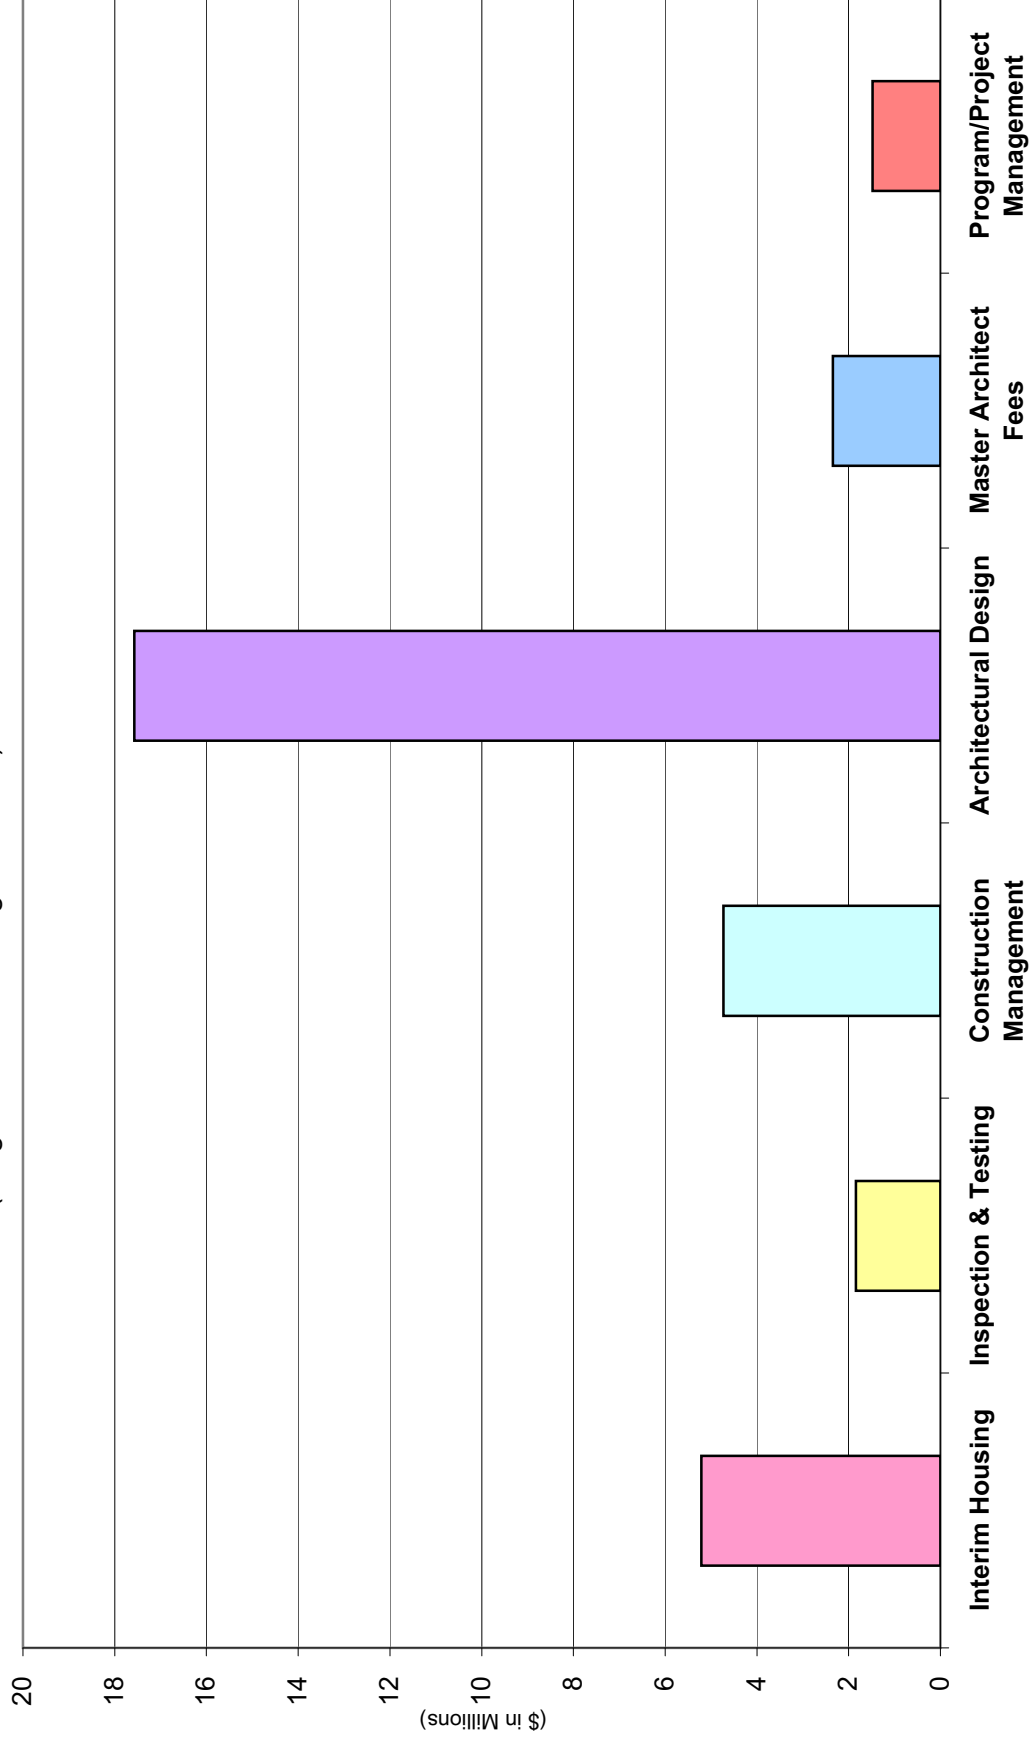


*Includes State School Facility Program Matching Funds

GUHSD PROP H* Actual Expenditures by Location
 (Program to date through 09/30/07) Total \$115.7M

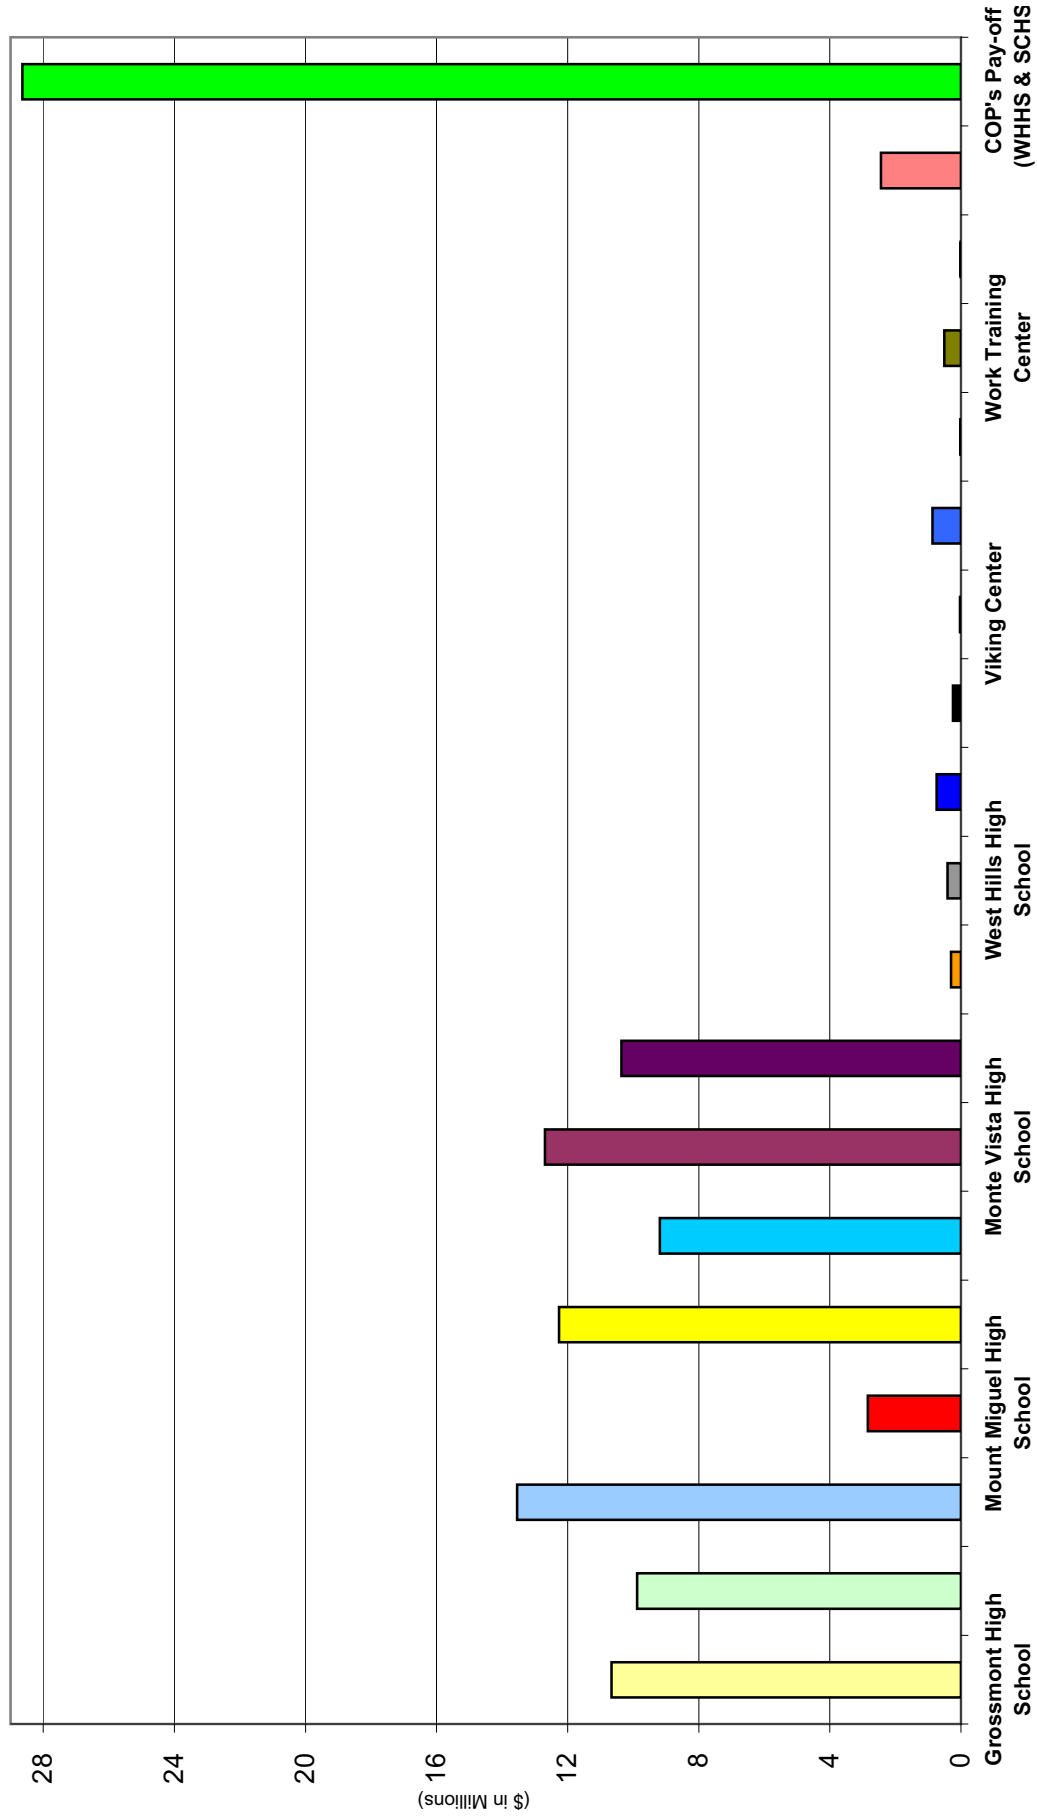


*Includes State School Facility Program Matching Funds

GUHSD PROP H* Actual Expenditures by Location Excluding COPs Pay-off
 (Program to date through 09/30/07) Total \$87.0M

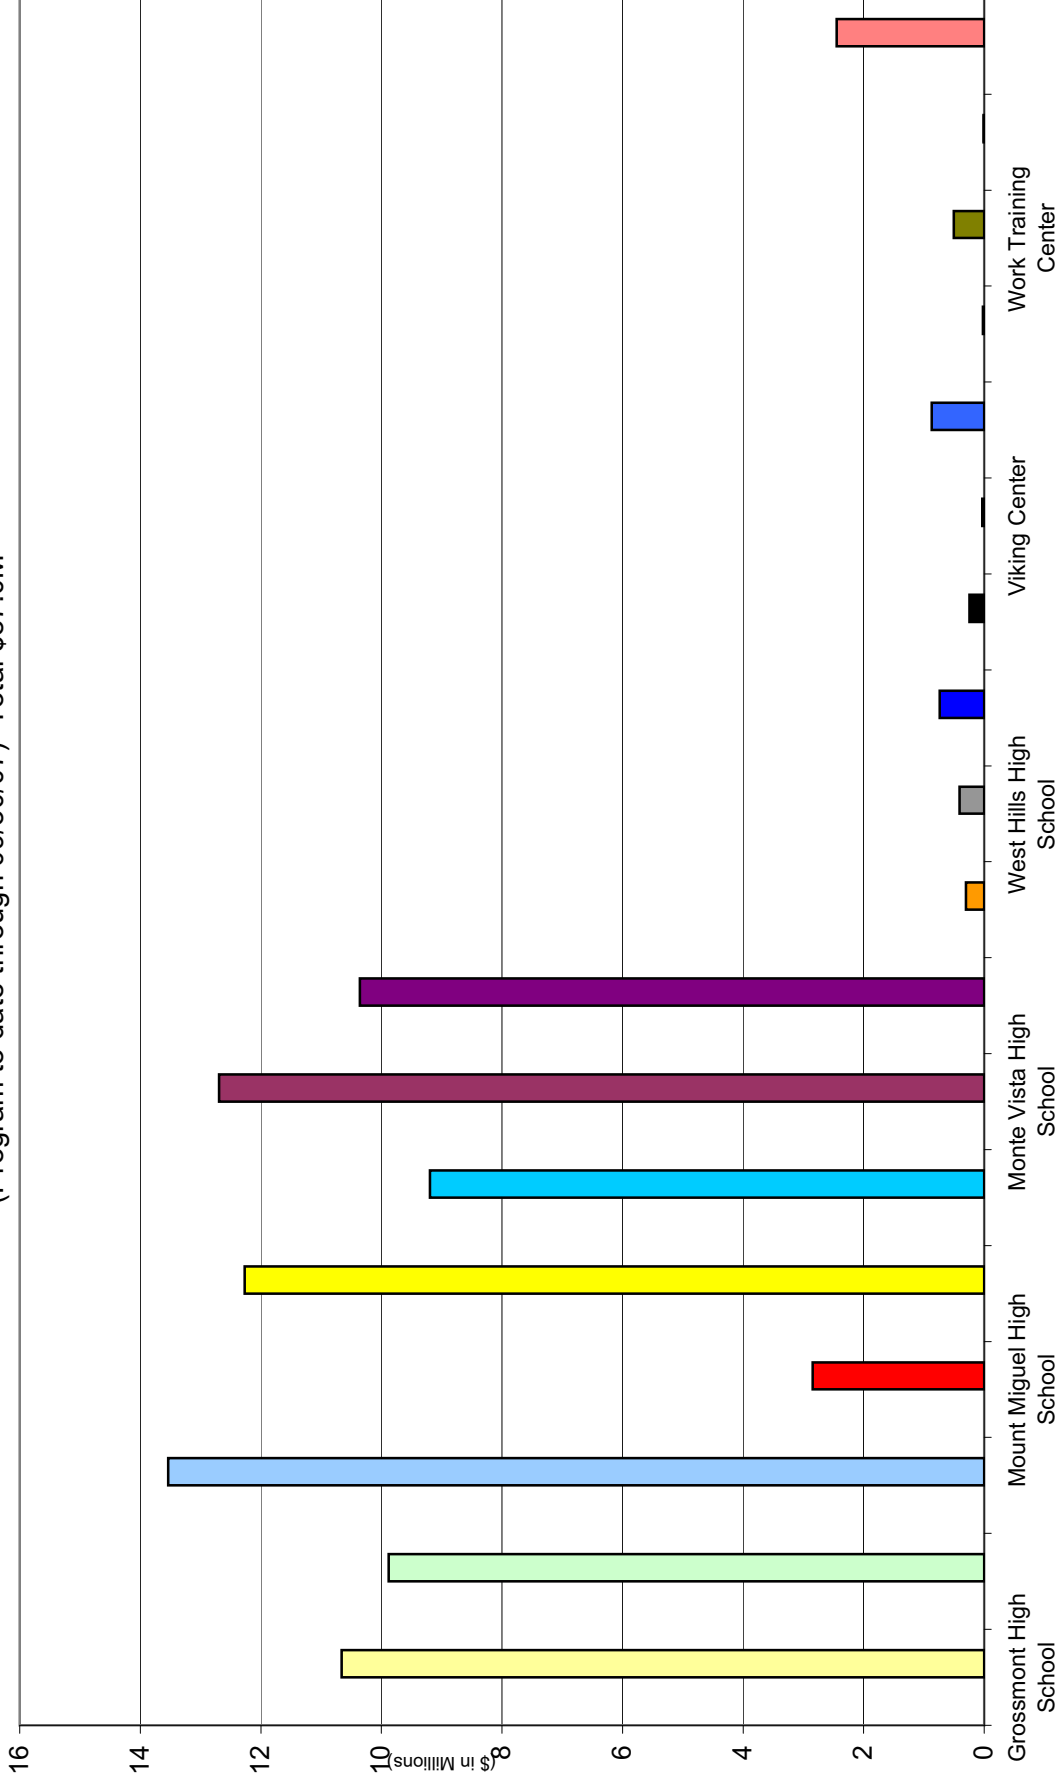

*Includes State School Facility Program Matching Funds

GUHSD PROP H* Actual Expenditures by Bond Element
 (Program to date through 09/30/07) Total \$115.7M

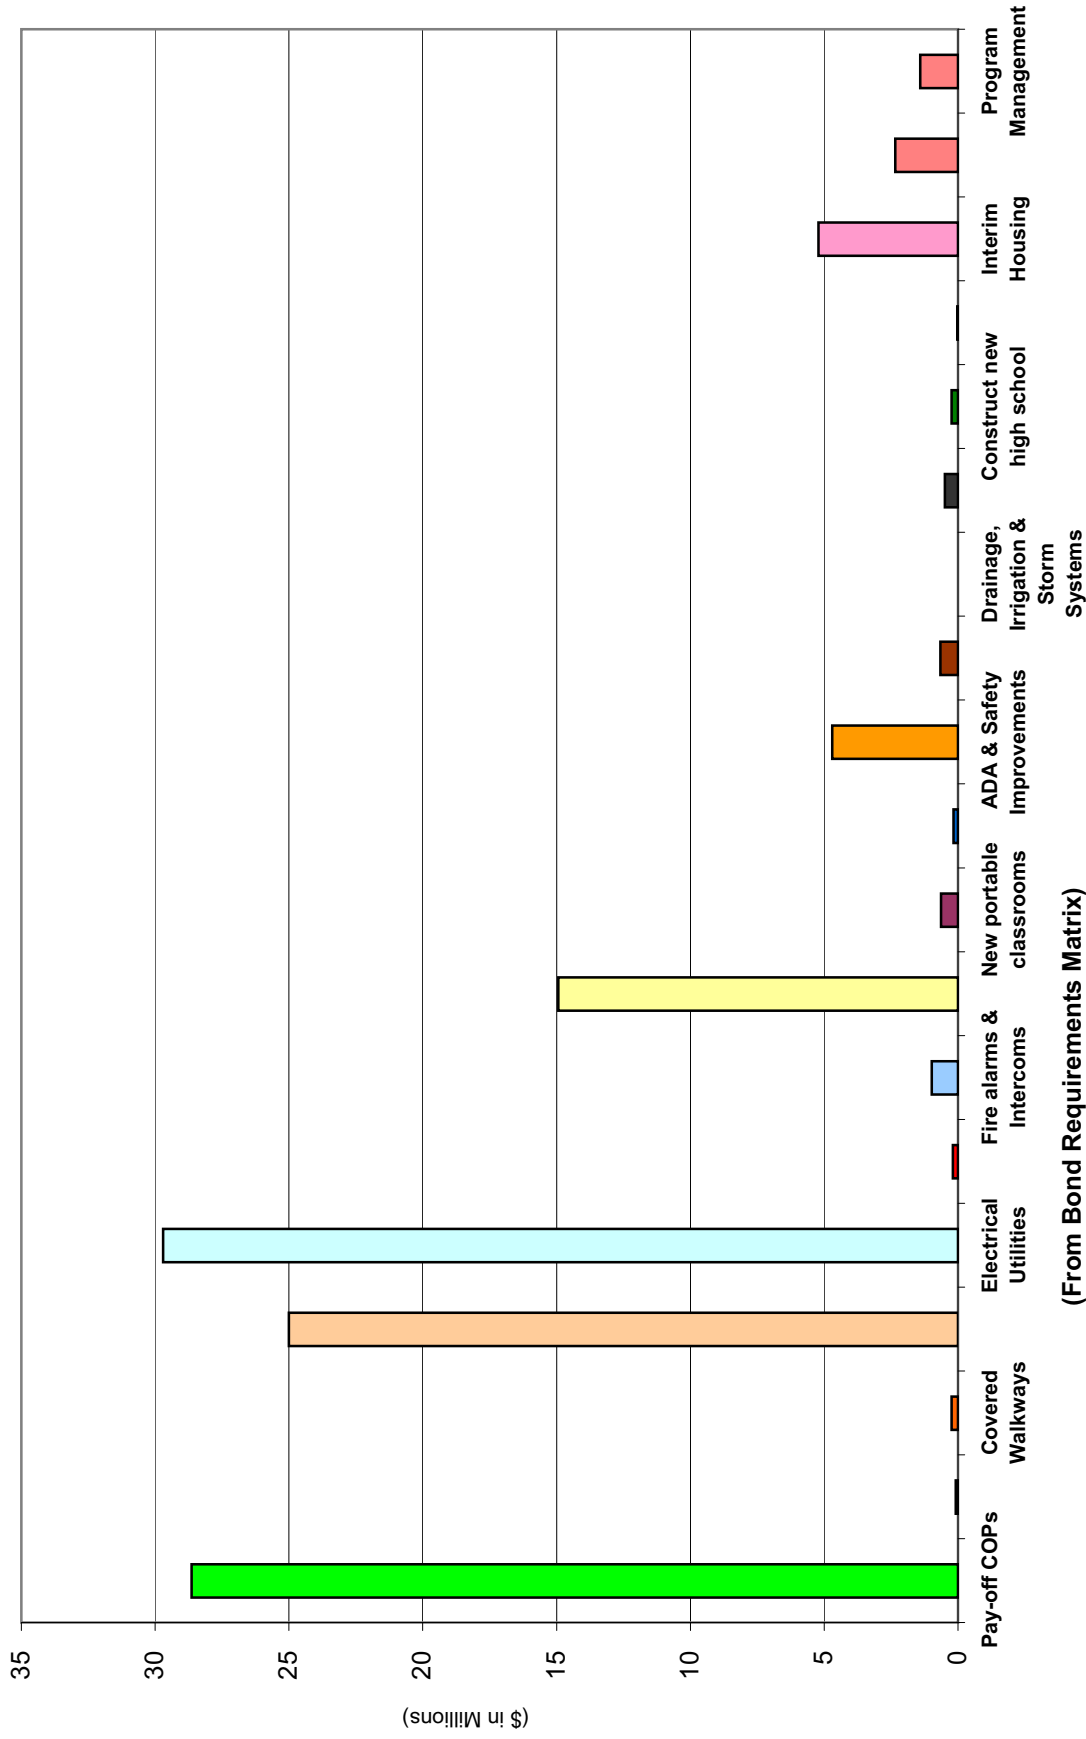

(From Bond Requirements Matrix)

GUHSD PROP H* Actual Expenditures by Bond Element Excluding COPs Pay-off & Infrastructure

(Program to date through 09/30/07) Total \$32.3M


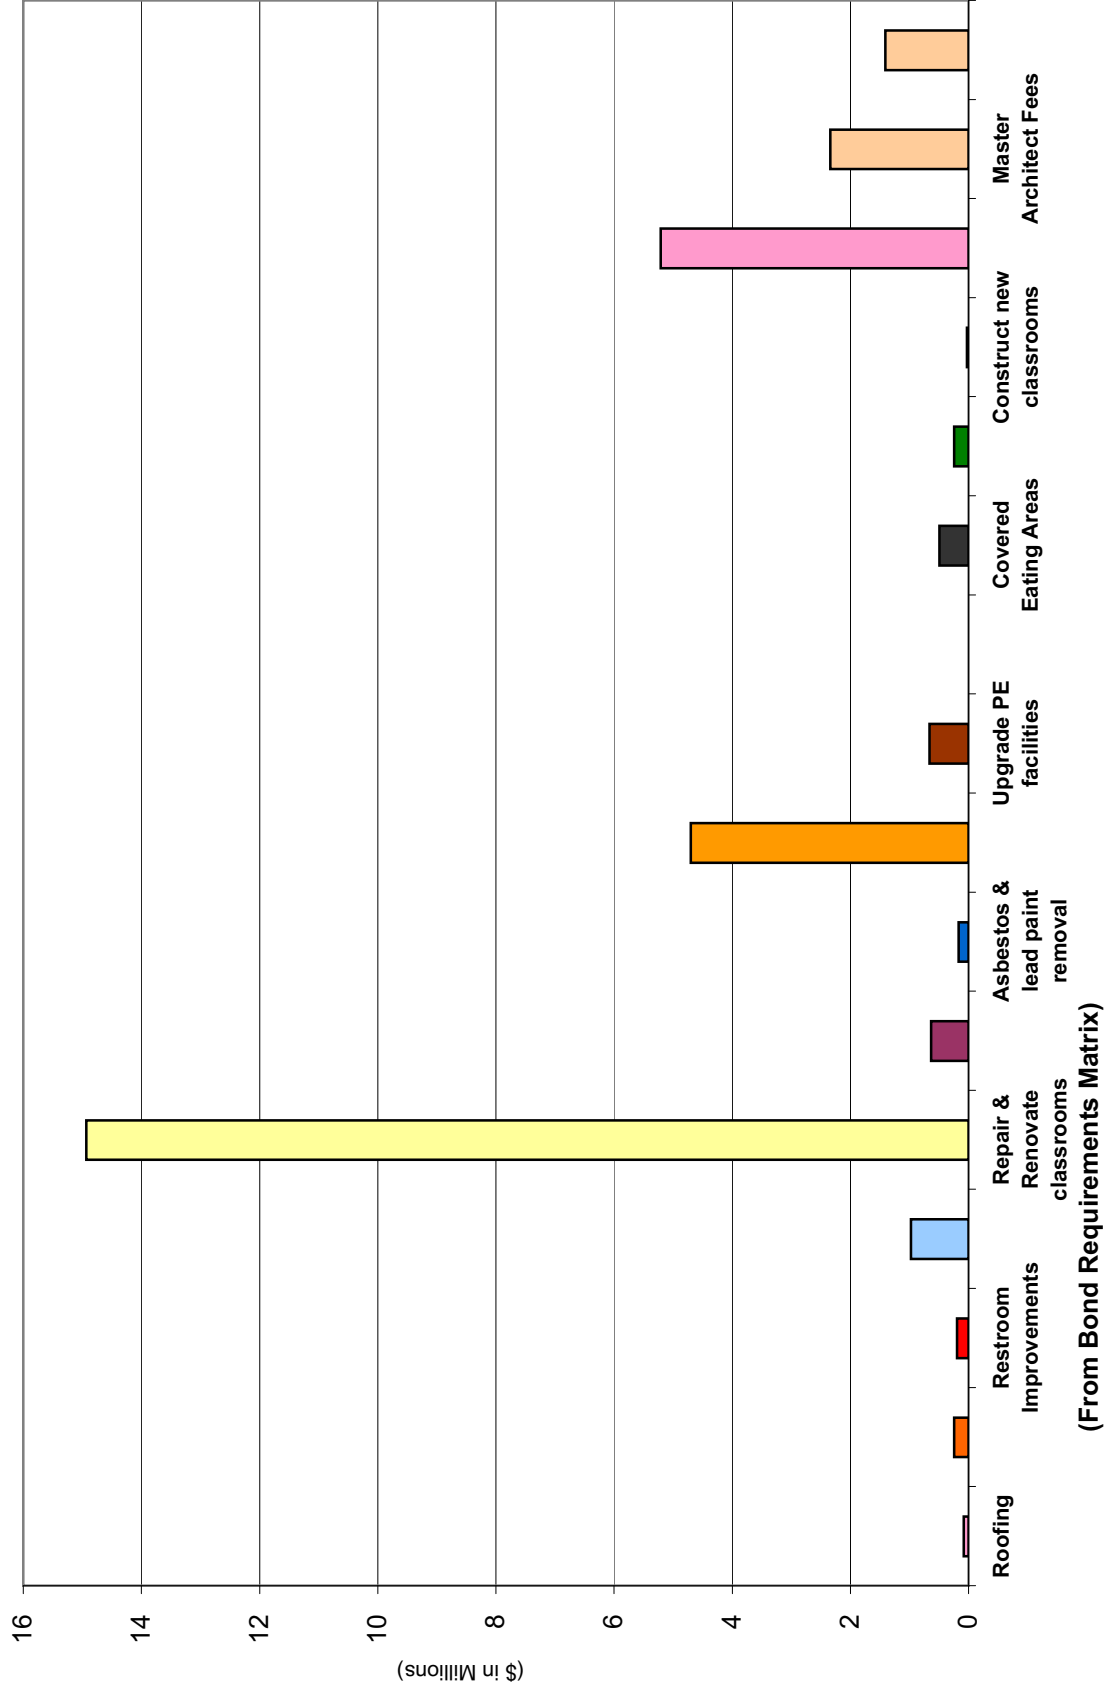


Exhibit 8.2

*Includes State School Facility Program Matching Funds


GUHSD Prop H* Program Management Organization Costs (Program to date through 9/30/07)

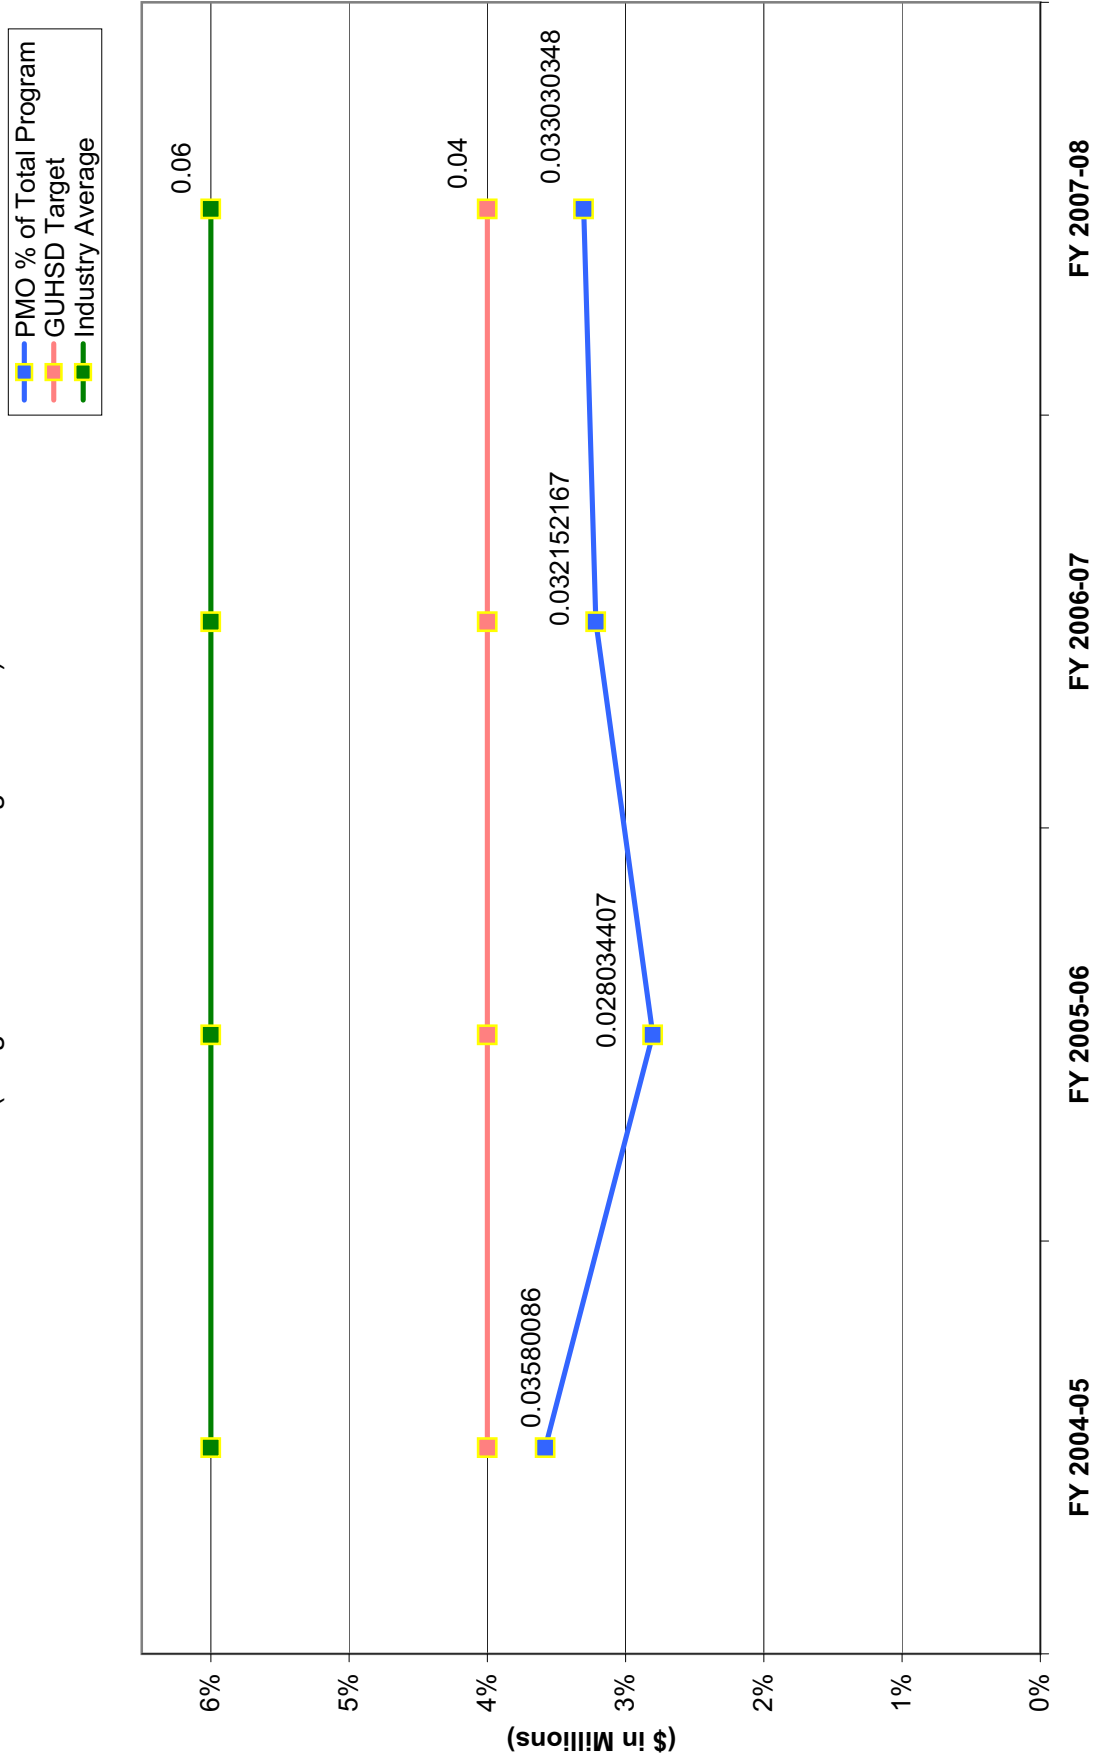

* Includes Prop H and State Matching Funds

GUHSD Prop H Construction Change Orders

(Program to date through 9/30/07)

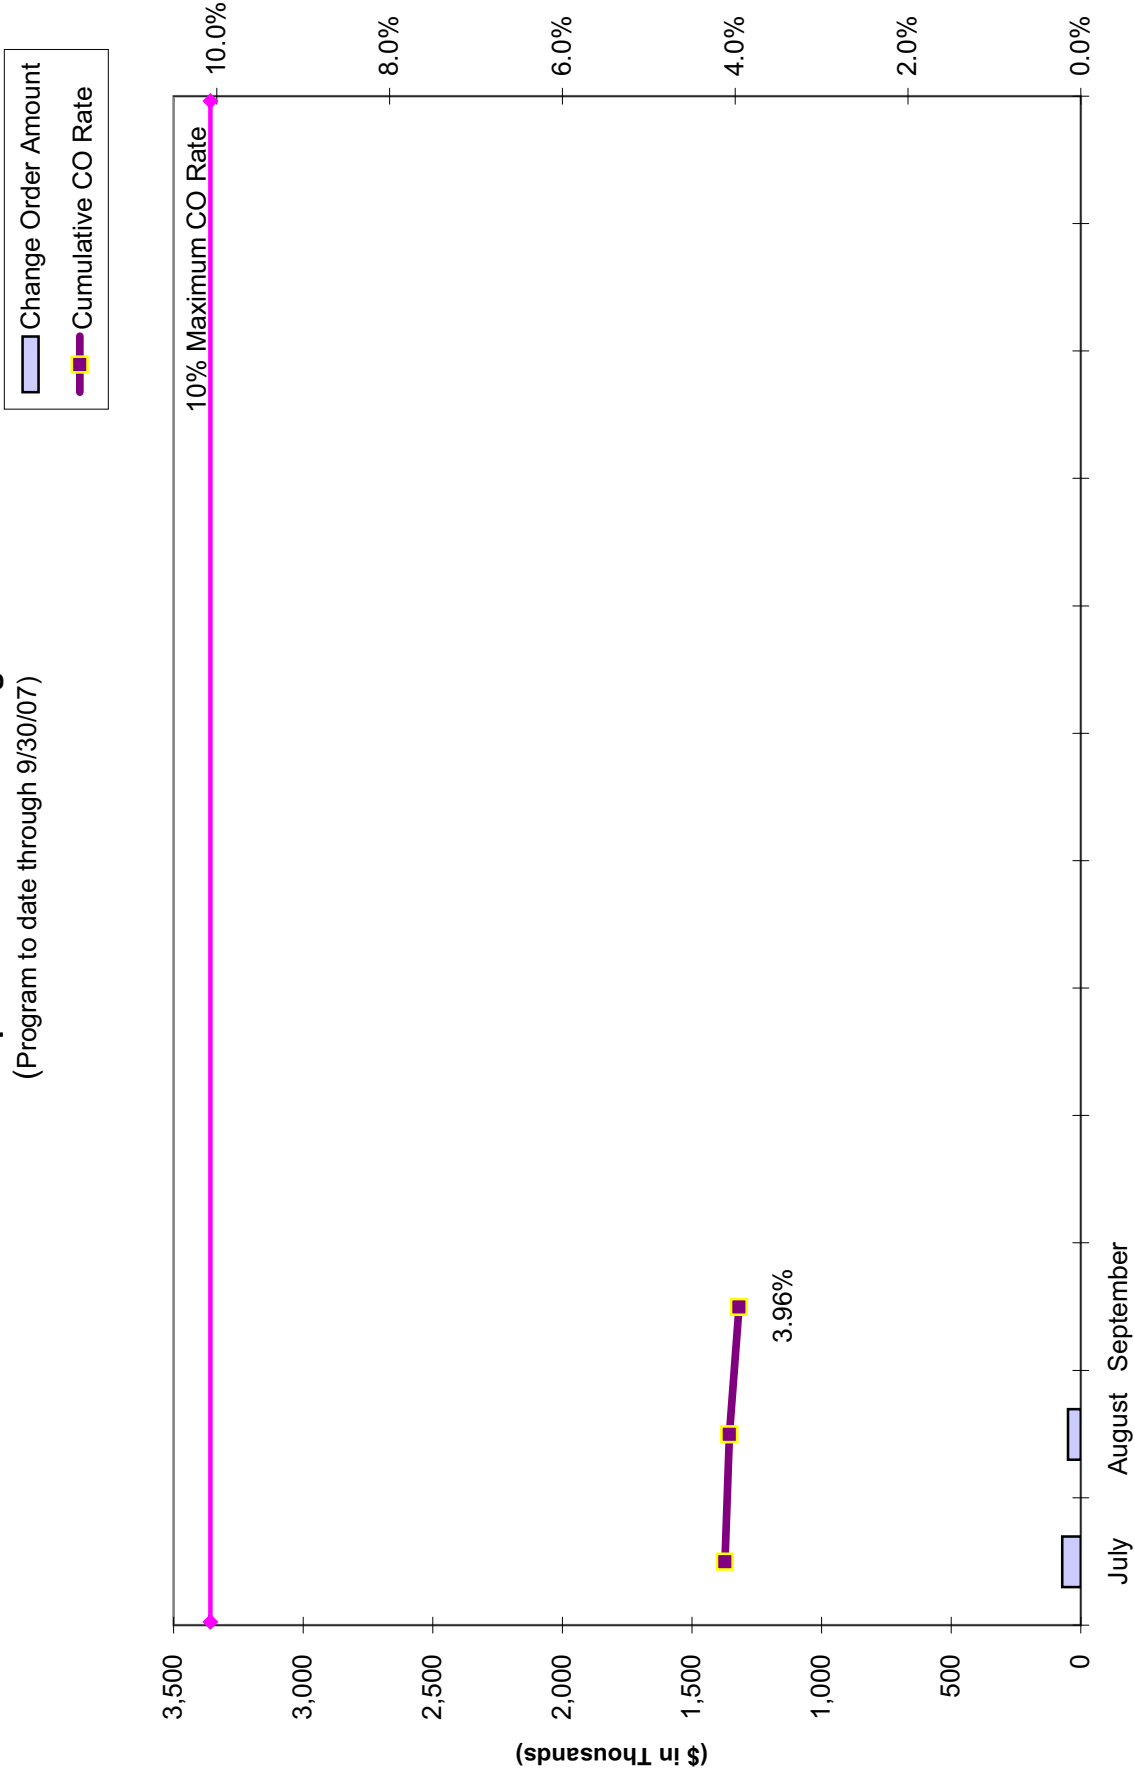

* Includes projects funded by Prop H and State Matching Funds



A. Appendices

DATA DATE:

Monday, November 05, 2007

Report # 03



PROP H SCHOOL WEEKLY ACTIVITY REPORT

FACILITIES MANAGEMENT DEPARTMENT

The purpose of this Prop H School Weekly Activity Report is to provide management within the District (District, Principals & staff) with a Weekly - Look Back/Look Ahead "SNAPSHOT" of activities of interest related to the construction projects.

EXISTING SCHOOLS

LOOK BACK/LOOK AHEAD ACTIVITIES

Grossmont High School (GHS) Phase 2B: Construction Phase 3A: Design	11/5/2007 - Phase 2B - Construction continuing on Building 800, with the current phase completion/occupancy impacted by the "wildfires". Phase 3A New Science Building - Harley Ellis Devereaux authorized to commence with the Schematic Design.
Helix High School (HHS) Phase 2B: Construction Phase 3A: Design	11/5/2007 - Phase 2B - Pre-demolition Construction Meeting taking place on Monday, 11/5/07. Construction to commence immediately. Phase 3A New Science Building - Harley Ellis Devereaux (Architect) authorized to commence with the Schematic Design.
El Cajon Valley High School (ECVHS) Phase 2B: Construction Phase 3A: Design	11/5/2007 - Phase 2B - Construction continuing on Building 500, with the current phase completion/occupancy delayed as a result of the "wildfires". Phase 3A New Science Building - final contract negotiations with HMC Architects to take place next 10 days.
Mount Miguel High School (MMHS) Phase 1A: Design Phase 2B: Design	11/5/2007 - Phase 1A - Architect is underway with the design of the underground utilities infrastructure. Phase 2B - Architect is underway with the design of the classroom modernizations.
El Capitan High School (ECHS) Phase 2B: Bid/Award Phase 3A: Design	11/5/2007 - Phase 2B - Board authorization to award contracts to lowest responsive bidders scheduled for 11/8/07. Phase 3A New Science Building - Harley Ellis Devereaux authorized to commence with the Schematic Design.
Granite Hills High School (GHHS) Phase 2B: Construction Phase 3A: Design	11/5/2007 - Phase 2B - Construction is underway. Phase 3A - New Science Building - conceptual phase complete. Final contract negotiations with HMC Architects to take place next 10 days.
Monte Vista High School (MVHS) Phase 2B: Bid/Award Phase 3A: Design	11/5/2007 - Phase 2B - Bid Opening was held on 10/30. Board authorization to award contracts to the lowest responsive bidders is scheduled for 11/8/07. Phase 3A - New Science Building - Harley Ellis Devereaux - authorized to commence with the Schematic Design.
Santana High School (SHS) Phase 2B: Bid/Award Phase 3A: Design	11/5/2007 - Phase 2B Bid opening delayed to 11/8/07 due to "wildfires". Phase 3A - New Science Building - Harley Ellis Devereaux - authorized to commence with the Schematic Design.
Valhalla High School (VHS) Phase 2B: Design Phase 3A/3BR: Design	11/5/2007 - Phase 2B/3A/3BR - A Preliminary Construction Budget has been established and issued to the Architect. A scope refinement meeting took place on Friday, 11/2.
West Hills High School (WHHS) Phase 2B: Design	11/5/2007 - Phase 2B - Design is continuing. Program Manager is validated the budget.
Steele Canyon High School (SCHS) Phase 2B: Design	11/5/2007 - Phase 2B - This project has commenced with the design phase. Program Manager is validating the budget.
Chaparral High School Phase 2B: Pre-Design	11/5/2007 - Phase 2B - This project is in the planning, pre-design phase. Program Manager is validating the budget.
Viking Center Phase 2B: Pre-Design	11/5/2007 - Phase 2B - A cost analysis of modernization vs. demolition replacement alternatives are currently being explored.
Homestead/Frontier School Phase 2B: Pre-Design	11/5/2007 - Phase 2B - This project is in the planning, pre-design phase. Program Manager is validating the budget.
Foothill Adult School Phase 2B: Pre-Design	11/5/2007 - Phase 2B - The project is in the final pre-design, scoping phase, with the Fire Alarm system identified as the scope of the Project.

DATA DATE:
Monday, November 05, 2007
Report # 03



PROP H SCHOOL WEEKLY ACTIVITY REPORT

FACILITIES MANAGEMENT DEPARTMENT

The purpose of this Prop H School Weekly Activity Report is to provide management within the District (District, Principals & staff) with a Weekly - Look Back/Look Ahead "SNAPSHOT" of activities of interest related to the construction projects.

Work Training Center Phase 2B: Pre-Design	11/5/2007 - Phase 2B - This project is in the planning, pre-design phase. Program Manager is validating the budget.
--	---

NEW SCHOOLS

LOOK BACK/LOOK AHEAD ACTIVITIES

New High School Phase: Planning	11/5/2007 - The CBOC has recommended that the Board authorize staff to hire a consultant to prepare a Demographics Study. Various sites are being evaluated. A Notice of Preparation (part of EIR process) was held on October 30th at the Alpine Community Center
--	--

PROGRAM HIGHLIGHTS:

Phase 2B projects are in construction at Grossmont High School, El Cajon High School, Granite Hills High School. With award recommendations for Phase 2B projects at El Capitan High School and Monte Vista High School anticipated later this week, the District will soon be in a "classroom modernization" construction phase unprecedented in the District's history. The Program Manager is still in the process of 1. Validating the Proposition H program; 2. Executing the 30 and 90 Day Action Plans, and 3. Developing the Recommended Path Forward.

LEGEND:

PRECONSTRUCTION PHASE(S)

- Planning
- Site Acquisition
- Pre-Design
- Design
- Pre-Bid
- Bid/Award

CONSTRUCTION PHASE(S)

- Construction
- Punchlist
- Close-outs

POST CONSTRUCTION

- Warranty Period

PREPARED BY:

FACILITIES MANAGEMENT



"A new momentum....a paradigm shift, creative execution"

Grossmont High School

Helix Charter High School

El Cajon Valley High School

Mount Miguel High School

El Capitan High School

Granite Hills High School

Monte Vista High School

Santana High School

Valhalla High School

West Hills High School

Steele Canyon High School

Chaparral High School

Viking Center

Homestead/Frontier School

Work Training Center

***...modernizing and constructing learning spaces for our children
...today and tomorrow.***

PROPOSITION H....FULL THROTTLE!!!
